
# **REPORT ON**

# REVIEW OF PROPOSED REDEVELOPMENT OF SEAWARD VILLAGE

# BY

# LIEUTENANT GENERAL (RETIRED) MARK EVANS AO, DSC

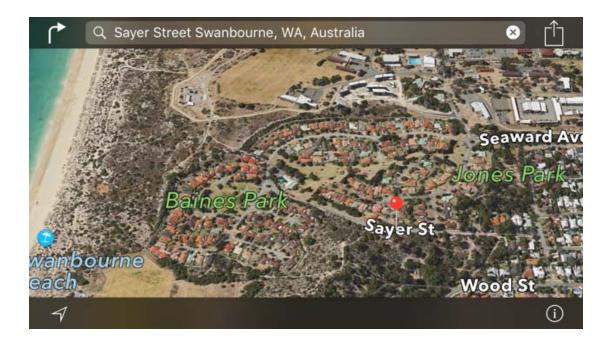

This document contains commercially sensitive information. The disclosure and use of this information may be subject to additional constraints.

# TABLE OF CONTENTS

| TERMS OF REFERENCE       5         EXECUTIVE SUMMARY       7         RECOMMENDATIONS       10         ACKNOWLEDGEMENT       11         INTRODUCTION       12         METHODOLOGY       15         BACKGROUND       16         DHA REDEVELOPMENT PROPOSAL       20         Proposed Redevelopment Concept       20         Proposed Redeveloped Seaward Village Residents.       21         Breakdown of redeveloped Seaward Village Areas       22         Land Use Observations       22         Proposed Program       23         Advantages       23         Disadvantages       23         Advantages       24         Stakeholder Engagement       24         Stakeholder Engagement       24         Submissions to the Review       26         Petition       28         Sucrity       30         Operational Capability       30         Social Impact in SASR       32 <th>LETTER OF TRANSMISSION</th> <th></th> | LETTER OF TRANSMISSION                                   |    |
|---|--|----|
| RECOMMENDATIONS10ACKNOWLEDGEMENT11INTRODUCTION12METHODOLOGY15BACKGROUND16DHA REDEVELOPMENT PROPOSAL20General20Proposed Redevelopment Concept20Undertakings to Seaward Village Residents21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Covenant29The Covenant30General30Operational Capability31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Environment36Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Valuation of the Refurbishment Option41Advantages41Disadvantages41Disadvantages41Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary45   | TERMS OF REFERENCE                                       | 5  |
| ACKNOWLEDGEMENT   |  |    |
| INTRODUCTION12METHODOLOGY15BACKGROUND16DHA REDEVELOPMENT PROPOSAL20General20Proposed Redevelopment Concept20Undertakings to Seaward Village Residents21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Joisadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer46Summary46  |  |    |
| METHODOLOGY15BACKGROUND16DHA REDEVELOPMENT PROPOSAL20General20Proposed Redevelopment Concept20Undertakings to Seaward Village Residents.21Breakdown of redeveloped Seaward Village Areas22Land Use Observations.22Proposed Program23Advantages.23Disadvantages.23Disadvantages.23Advantages.24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Covenant30Operational Capability30Security31Encroachment and Noise32Child Care33Summary34Broader Community Issues35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer46Summary46  | ACKNOWLEDGEMENT  | 11 |
| BACKGROUND16DHA REDEVELOPMENT PROPOSAL20General20Proposed Redevelopment Concept20Undertakings to Seaward Village Residents21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Social Impact in SASR32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment.35Farffic36Risks.37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Disadvantages41Disadvantages42Model 3 - Ownership Transfer44Summary46   | INTRODUCTION   | 12 |
| DHA REDEVELOPMENT PROPOSAL20General20Proposed Redevelopment Concept20Undertakings to Seaward Village Residents.21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Social Impact in SASR35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Valuation of the Refurbishment Option41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost46   | METHODOLOGY  | 15 |
| General20Proposed Redevelopment Concept20Undertakings to Seaward Village Residents21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Fardific36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | BACKGROUND   | 16 |
| Proposed Redevelopment Concept20Undertakings to Seaward Village Residents.21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Covenant29The Covenant30General30Operational Capability30Security31Encroachment and Noise32Child Care33Summary34Broader Community Issues35Environment35Environment36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | DHA REDEVELOPMENT PROPOSAL                               | 20 |
| Undertakings to Seaward Village Residents21Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Environment36Optics37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Sutability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  |  |    |
| Breakdown of redeveloped Seaward Village Areas22Land Use Observations22Proposed Program23Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Proposed Redevelopment Concept                           | 20 |
| Land Use Observations22Proposed Program23Advantages23Disadvantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Undertakings to Seaward Village Residents                | 21 |
| Proposed Program23Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer46   | Breakdown of redeveloped Seaward Village Areas           | 22 |
| Advantages23Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Snared Cost43Model 3 - Ownership Transfer44Summary46  | Land Use Observations                                    | 22 |
| Disadvantages23Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Proposed Program   | 23 |
| Approval Process Risks24KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Advantages   | 23 |
| KEY ISSUES ARISING FROM REDEVELOPMENT24Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  |  |    |
| Stakeholder Engagement24Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost.43Model 3 - Ownership Transfer44Summary.46  | Approval Process Risks                                   | 24 |
| Submissions to the Review26Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | KEY ISSUES ARISING FROM REDEVELOPMENT                    | 24 |
| Petition28Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Stakeholder Engagement                                   | 24 |
| Summary28The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Submissions to the Review                                | 26 |
| The Covenant29The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Petition   | 28 |
| The Nexus with SASR30General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Summary  | 28 |
| General30Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | The Covenant   | 29 |
| Operational Capability30Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | The Nexus with SASR                                      | 30 |
| Security31Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost.43Model 3 - Ownership Transfer44Summary46  | General  | 30 |
| Encroachment and Noise32Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Operational Capability                                   | 30 |
| Social Impact in SASR32Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Security   | 31 |
| Child Care33Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Encroachment and Noise                                   | 32 |
| Summary34Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Social Impact in SASR                                    | 32 |
| Broader Community Issues35Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Child Care   | 33 |
| Environment35Traffic36Risks37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Summary  | 34 |
| Traffic36Risks.37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Broader Community Issues                                 | 35 |
| Risks.37A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Environment  | 35 |
| A FEASIBLE ALTERNATIVE - REFURBISHMENT38Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Traffic  | 36 |
| Refurbishing DHA Houses39Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  |  |    |
| Suitability of Seaward Village Housing for Refurbishment40Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | A FEASIBLE ALTERNATIVE - REFURBISHMENT                   | 38 |
| Evaluation of the Refurbishment Option41Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Refurbishing DHA Houses                                  | 39 |
| Advantages41Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Suitability of Seaward Village Housing for Refurbishment | 40 |
| Disadvantages42Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46   | Evaluation of the Refurbishment Option                   | 41 |
| Model 1 - DHA Fund Upgrade43Model 2 - Shared Cost43Model 3 - Ownership Transfer44Summary46  | Advantages   | 41 |
| Model 2 – Shared Cost   | Disadvantages  | 42 |
| Model 3 – Ownership Transfer  |  |    |
| Summary   | Model 2 – Shared Cost                                    | 43 |
|   | Model 3 – Ownership Transfer                             | 44 |
| COST COMPARISON 46  |  |    |
|   | COST COMPARISON  | 46 |





# 3

| Background Information                 | 46 |
|--|----|
| Basis for Costs - Redevelopment Option | 46 |
| Refurbishment Initial Cost Estimates   | 47 |
| Basis for Costs - Refurbishment Option | 48 |
| JLL Valuation Critique                 | 49 |
| Summary                                | 49 |
| RELATIVE MERITS                        |    |
| Redevelopment                          | 50 |
| Refurbishment                          | 50 |
| Table - Comparison of Key Elements     | 51 |
| Summary                                |    |
| CONCLUSION                             | 53 |
| RECOMMENDATIONS                        | 54 |

## Annexes:

| А | Deed of Covenant   |  |
|---|--|--|
| В | DHA Submission – Seaward Village Review dated 15 January 2016  |  |
| С | DHA Project Financials Seaward Village Review dated 15 January |  |
|   | 2016 (Commercial-in-Confidence)                                |  |
| D | DHA Revised Project Financials Seaward Village Review dated 3  |  |
|   | February 2016 (Commercial-in-Confidence)                       |  |
| Е | DHA Seaward Village – 5 Year Refurbishment Feasibility Costing |  |
|   | dated 16 February 2016 (Commercial-in-Confidence)              |  |
| F | Submissions to the Review                                      |  |

# **Enclosure:**

1. Jones Lang La Salle (ACT) Pty Ltd Valuation Critique Seaward Village Western Australia as at February 2016 (Commercial-in-Confidence and Confidential to the Department of Defence) 4

# LETTER OF TRANSMISSION

# **Review of Proposed Redevelopment of Seaward Village**

The Hon Michael McCormack MP Assistant Minister for Defence Parliament House CANBERRA ACT 2600

Dear Minister

I am pleased to present my report of the Review I have conducted into the Proposed Redevelopment of Seaward Village.

The Review was conducted in accordance with the Terms of Reference approved by the Assistant Minister for Defence on 26 November 2015.

I ask that you note Annexes C, D and E of the report contain information provided by Defence Housing Australia (DHA) which is commercial-in-confidence. This cost breakdown information is also included in parts of the report. Similarly, Enclosure 1, a Valuation Critique of the DHA costs, conducted by Jones Lang LaSalle (JLL) (ACT) Pty Ltd is commercial-in-confidence and confidential to the Department of Defence. Should you decide to publically release the report, I recommend that Annexes C, D and E and Enclosure 1 not be released and that all information in the report relating to these be redacted.

Submissions to the Review are included separately at Annex F. This information has been collected without express consent being given to the public disclosure of personal information contained in the submissions and should be managed in accordance with *Australian Privacy Principles* under the *Privacy Act 1988*.

May I take this opportunity to acknowledge DHA and Defence for their professional support to me during the conduct of my Review. I also wish to recognise the many people and organisations that provided valuable and informative submissions and representations that assisted me during the Review.

s22

Mark Evans AO DSC Lieutenant General (Retired)

25 February 2016

# 5

# Review of Proposed Redevelopment of Seaward Village

# **TERMS OF REFERENCE**

Defence provides housing assistance to support capability by ensuring that ADF members and their families have access to housing that meets or exceeds community standards in reasonable proximity to the member's place of duty. Housing assistance also compensates for the housing detriment that arises from the requirement for ADF members to frequently relocate, by providing a subsidy to reduce the overall cost of house rental to members and to offset differences between high and low cost locations.

The primary form of housing assistance provided to members with dependants is in the form of a Service Residence, formerly known as a Married Quarter, managed by Defence Housing Australia (DHA). If a Service Residence is unavailable, a member may receive Rent Allowance to find accommodation of similar value in the private rental market.

Seaward Village is an estate of 153 Service Residences adjoining Campbell Barracks in the Perth suburb of Swanbourne. The Village houses approximately 25% of the members of the SASR and their families along with a number of families from other Army and Joint units in the Perth area.

Seaward Village is owned by DHA, but subject to a Deed of Covenant that prevents DHA from selling of leasing any of the land to private citizens without the agreement of Defence. Roads and parks within Seaward Village are owned and maintained by local and State authorities.

The residences in Seaward Village were constructed in 1991. Many are now not compliant with Defence standards and would require significant work to bring up to standard. As a result, Defence and DHA have agreed in principle to redevelop the village to provide an increased amount of contemporary housing with a longer lifespan, and to also remediate ageing civil infrastructure within the Village. The current proposal seeks to substantially fund the redevelopment through the sale of not more than 25 per cent of the Village.

The Government has commissioned this Review to evaluate the present proposal for redevelopment and its effectiveness in delivering quality, long-term and sustainable housing for ADF members and their families, and to advise if there are any alternative options that may deliver a similar or superior outcome.

The Review is to assess the existing redevelopment proposal and feasible alternative options regarding the redevelopment of Seaward Village to provide a long-term housing solution for Campbell Barracks and other nearby Defence establishments. Regard should be given to:

a. The relative merit of a refurbishment program versus redevelopment.

# FOUO

- 6
- b. Security the impact of the proposed development plan on the security of Campbell Barracks and on the personal security of the residents.
- c. Social Impact.
- d. requirement for a covenant to restrict future transactions in the land.

The Review may take submissions from (but not limited to) Defence, DHA, the State Government, the local Council, the SAS Association, Seaward Village residents, the Friends of Allen Park, the neighbouring civilian community and other parties that the Review considers to have a direct and legitimate interest in the redevelopment proposal. The Review may further consult with the same where necessary to clarify matters covered by a submission, or to otherwise progress the Review.

The Review is to provide a written report to the Government no later than 29 February 2016

## 7

# **EXECUTIVE SUMMARY**

1. This Review was established to 'evaluate the present proposal for redevelopment and its effectiveness in delivering quality, long term and sustainable housing for ADF members and their families, and to advise if there are any alternative options that may deliver a similar or superior outcome.<sup>1</sup>

2. Critical to comprehending the current issues associated with Seaward Village (the Village) redevelopment is an understanding of the nature of the terrain surrounding Campbell Barracks at Swanbourne, the unique role and tasks of the Special Air Service Regiment (SASR); the needs of ADF families living in the Village; and the relationship of the unit and families to the local communities.

3. The Village is a small estate of 153 Service Residences (SRs) in Perth that is owned by Defence Housing Australia (DHA). It is immediately adjacent to Campbell Barracks, the operational home of the SASR and is mostly occupied by SASR posted personnel and their families.

4. In 1992, ownership of the land in the Village and 43 houses that existed at the time was transferred from Defence to DHA. These houses do not comply with the minimum standards prescribed in Defence policy and should be upgraded or replaced by 2017. After 1992, an additional 110 houses were constructed in the Village. They are compliant but require upgrading. While they are owned by DHA, a Deed of Covenant (the Covenant) was established in 2001 that prevents DHA from selling or leasing the properties to civilians. This Covenant, which is unique to the Village, places constraints on how DHA manages the Village and precludes the application of the DHA business model, i.e. sale and leaseback.

5. DHA has developed plans to provide modern housing in the Village for ADF members and their families. Under the proposal, the existing homes would be demolished, allowing redevelopment of the land and construction of 165 modern houses, along with new streets, parkland areas and a new Child Care Centre. To fund the project, the Government, Secretary of the Department of Defence and the Chief of the Defence Force (CDF) agreed that DHA could sell 25% of the total site area to the public. The sale of developed housing lots to the private market would partly offset the significant cost of the redevelopment, with the balance of <sup>\$47</sup> funded by DHA. There would be no requirement for Defence or Government funding. The project, on current projections, is planned to be complete by 2022.

6. The DHA concept of redevelopment and partial sale of the Village has met with unforeseen and considerable opposition from stakeholders groups and individuals. While it is not unusual for there to be resistance to large projects such as this, generally attitudes soften over time after the benefits of the project become more widely recognised and accepted. This has not been the case in this instance. Resistance has strengthened and the basis for criticism has become more informed. As a result, the Assistant Minister requested a Review of the redevelopment proposal

<sup>&</sup>lt;sup>1</sup> Terms of Reference

8

and the general public were invited to make submissions. Other than the DHA submissions, the Review received 84 submissions from groups and individuals who, without exception, opposed the redevelopment proposal. An on-line Petition to the Review: '*Protect Seaward Village and Save Allen Park*,' was endorsed by 575 supporters.

7. During the Review, key issues were evident regarding the redevelopment related to SASR, in particular to its operational capability, morale, security, encroachment and noise, social impact and child care. In addition there is strong opposition to the proposed redevelopment from local Government, communities and interest groups, primarily focused on the merits of the proposal; poor communication of the project; disruption to ADF families; adverse impacts on the local environment and Allen Park; and the increased flow of traffic into Sayer Street and the surrounding neighbourhood.

8. The Review has considered in detail an alternative option of refurbishing the existing housing stock. A refurbishment program could improve amenities and provide additional rooms (such as extended living areas and ensuites); replace old appliances, fixtures and fittings and generally improve the amenity of the houses. The refurbished houses would be high quality with an economic life span of 30 years. The refurbishment would be carried out through a rolling program with a limited number of houses off line at any one time, causing less disruption to families. However, a thorough survey of the properties has not been conducted and this would be necessary to determine the extent of work required for each house before refurbishment could be progressed.

9. The refurbishment option is less complex than redevelopment, allows continued occupation of most of the Village throughout the project and takes less time to complete. While new houses would not be provided and most of the limitations of the current houses would remain, they would meet the Defence minimum standard and be of good quality. DHA has a reputation for providing high quality results from refurbishment programs.

10. It is possible that a number of older houses would be deemed unsuitable for refurbishment and replacement houses would be required. That number would be determined following the survey of the properties.

# s47(1)(b) - commercially valuable information

9

# s47(1)(b) - commercially valuable information

13. The merits of the redevelopment proposal were considered against the alternative of refurbishment. This confirmed that proceeding with the agreed proposal of redevelopment is feasible. Defence members would have new homes in the Village with the costs and risks shouldered by DHA. To achieve this, the Covenant would be lifted; at least 25% of the Village would be sold to developers; 153 brick homes would be demolished; numerous Defence families would be relocated and 165 SRs would be rebuilt over a period of about six years; followed by construction of about 140 civilian houses in due course. There are a number of risks with this option.

14. If a decision is made to proceed with redevelopment, it is likely that the position of those stakeholders who oppose it will harden and a more active and coordinated campaign against redevelopment is possible. In addition, DHA is at the beginning of a development process and has no guarantee of bringing the project to successful conclusion in its journey through State Lands and Planning Departments and City of Nedlands Council processes. Also, the potential closure of Sayer Street as an egress point to the Village is unresolved.

15. The alternative refurbishment option provides an opportunity to address operational capability, sustainability, and community issues more holistically. This option is feasible. It would retain the integrity of the Village as intended by the Covenant. It would not provide the same modernity and quantity of houses that the rebuild would achieve. The homes would be upgraded to a good condition but would remain essentially 1980/90 brick homes meeting the agreed standard. This limitation is offset by proximity to work and amenities, and a sense of security and community.

16. DHA has not provided a complete and comprehensive picture of the state of housing stock in the Village. Therefore, it is possible that a refurbishment option will cost more than the potential net redevelopment cost predicted. It could also cost less. This option would not produce modern homes, albeit some homes would be replaced. However; a high quality outcome could be achieved with the current stock, which if maintained in a sustainable way, could provide an outcome that is aligned with future intentions for the redevelopment of Campbell Barracks. Refurbishment would certainly reduce much of the friction that has developed progressing the redevelopment option and achieve quick wins. It also has fewer risks in achieving an acceptable outcome for all key stakeholders.

17. The Covenant created a unique model for Defence and DHA to manage. It purposely placed a constraint on DHA that limited its management options for the Village. In essence this was part of doing business with Defence. It was not intended its business model would apply in this instance to provide 'adequate and suitable housing.' This was a cost that had to be borne. Notwithstanding it created a significant tension for DHA in terms of their main function directed in the *DHA Act* 

#### 10

and its requirements to act as a Government Business Enterprise (GBE). This is a significant issue that rests outside the TOR but needs addressing in due course.

18. As a result of the DHA wish to apply its business model, there appears to have been a reluctance to invest in improving the Village to any great extent, indicated by the cessation of a refurbishment program that was under way in 2012. The redevelopment concept was then presented to Defence without a complete analysis of the state of the existing houses and no documentation was provided to confirm a thorough identification of risks. The proposal was certainly attractive in terms of achieving the original aim of new housing for ADF members and families, with the added incentive of costs and risks being borne largely by DHA. It could be argued that, during planning, insufficient weight was placed on non financial factors, such as the geography of the Village, the state of existing houses, connection of the Village to significant operational capability, its position and relationship to communities inside the City of Nedlands, and possible adverse reactions to a redevelopment proposal from key stakeholders.

19. The options of redevelopment and refurbishment are both feasible. However, given the difficulties that have arisen during the redevelopment process this option is arguably beyond the culmination point for success. If it is progressed DHA will almost certainly have to 'reset' and start again with a new process of consultation, collaboration and communication. It will continue to be bedevilled by the issues raised in this report. Fundamentally, the 'hearts and minds' campaign has been lost by DHA. Refurbishment is a more conservative approach and would achieve similar results i.e. a quality, long term and sustainable housing solution but importantly it is also likely to produce a superior overall outcome.

20. On its merits, refurbishment is an option that carries less complexities and less risk. Refurbishment is recommended. The challenge is to ensure that, if refurbishment is selected, the same issues do not arise in another 10 to 15 years. The paper provides three models for consideration as to how refurbishment may be taken forward. A long term approach may be to consider the transfer of Seaward Village from DHA to Defence in due course.

# RECOMMENDATIONS

21. Following a thorough review of all available information, the following recommendations are made:

- The redevelopment of Seaward Village should not proceed
- The Covenant should remain in place and the sale of land in Seaward Village should not be considered in the short to mid term
- A refurbishment program for Seaward Village should be initiated as soon as possible, designed to provide high quality refurbished houses and reduce disruption to ADF members and their families
- Consideration should be given to ownership transfer of Seaward Village from DHA to Defence in the long term
- Robust communication strategies should be developed to support the refurbishment program

#### FOI 198/20/21 Report

#### FOUO

#### 11

# ACKNOWLEDGEMENT

The Review wishes to acknowledge with thanks the information and assistance provided by the following during the course of the Review:

Minister J Bishop Liberal Member for Curtin Senator D Smith WA Liberal Liberal Member for Canning The Hon A Hastie The Hon C Barnett WA Premier, Member for Cottesloe Mr D Richardson Secretary Department of Defence MAJGEN F McLachlan AHQ MAJGEN J Sengelman SOCAUST Mr S Grzeskowiak DEPSECEIG Mr P Prior CFO Mr D Spouse FAS FS Mr P Hetherington A/FAS RA Mr P Way DGDCO Mrs R Ritchie NC DFA **RADM B Wolski** DGWP Ms J Greig A/FAS PPC&D **BRIG N Beutel** DGCF&I **COL S Davies** DSOD Mr Martin Moseley DSA SAS Regiment CO, XO, members and families The Hon JAL (Sandy) MacDonald Chairman DHA Ms J Mason Acting Managing Director, DHA Mr M Brady DHA Board Member Ms M Dermatossian COO DHA Mr J Dietz GM PPG DHA Mr V Gallagher GM S&I DHA Mr J Wallace DHA Mr S Imrie Partner, HWL Ebsworth Lawyers Mr M Shadbolt Director, Valuations & Advisory, Jones Lang LaSalle (ACT) Pty Ltd

WA Department of Lands WA Department of Planning City of Nedlands Council Seaward Village Working Group National Chairman Australian Special Air Services Association Friends of Allen Park Friends of Allen Park Bushland Group Sayer Street Residents Swanbourne Coastal Alliance Inc Group All other groups and individuals who made submissions and petitions to the Review

#### FOUO

#### FOI 198/20/21 Report

# 12

# REVIEW OF PROPOSED REDEVELOPMENT OF SEAWARD VILLAGE

#### **References:**

- A. Defence Housing Australia Act (1987) (as amended)
- B. Defence/DHA Joint Working Party Report dated 10 November 2010
- C. Services Agreement on Housing and Related Matters dated 2006 (as amended)
- D. DHA Perth Housing Survey Report of September 2015

# **INTRODUCTION**

1. Critical to comprehending the current issues associated with Seaward Village (the Village) redevelopment is an understanding of the nature of the terrain surrounding Campbell Barracks at Swanbourne, the unique role and tasks of the Special Air Service Regiment (SASR); ADF families living in the Village; and the close relationship of the unit and families to the local communities.

2. The Village is a small estate of 153 service residences (SRs) owned by Defence Housing Australia (DHA). It is nestled in a horse-shoe shaped valley in coastal parkland overlooking the Indian Ocean at Swanbourne in Perth, Western Australia (WA). It was developed on and occupies approximately 21 hectares of sandy undulating terrain that is dominated by Melon Hill, a feature that abuts its south-eastern boundary. The Village is bordered to its south by about 18 hectares of parkland, known as Allen Park, and immediately adjacent to its north is Campbell Barracks, that has been the operational home of SASR for nearly 60 years. The Village is accessed by only two roads: Seaward Avenue (primary access) and Sayer Street. While not closed to the public its geography provides a notable degree of security and privacy to its residents. It is mostly occupied by SASR posted personnel and their families.

3. Since 1999, the SASR has been almost continuously on operations. It has proportionally done much of the operational heavy lifting for the ADF and the Government and is still heavily committed in the Middle East. If not actively on operations, over 60% of the unit at any one time is at very short degrees of notice to move. Many deploy on exercises, training and operations at short notice and experience absence from families for extended periods of time. Its operational tempo is significantly higher than most other organisations in Defence.

4. The nature of SASR work is such that it is operationally necessary for many members to live in close proximity to Campbell Barracks. At the time of writing this report approximately 93 SASR members live at the Village. The remaining houses are occupied by Defence families posted to the metropolitan area of Perth, some with special needs. An increasing number of houses are becoming vacant due to the redevelopment project. At present, 34 SASR families receive Rent Allowance. 13

5. Over the years the Village has been described as part of the '*Campbell Barracks - Seaward Village Zone*<sup>2</sup> that has provided real and intangible benefits operationally, socially and for the broader community. It is regarded as intrinsic to SASR capability, providing: housing close to work, commensurate with high readiness requirements; a sense of security for families; social cohesion and support, particularly in periods of operational commitments and training activities during which the Special Forces (SF) have sustained a high proportion of ADF casualties; and reassurance for deployed soldiers regarding the welfare of their families during their absence.

6. The Village exists within a broader community in Postcode 6010 that includes the suburbs of Nedlands, Mount Claremont, Swanbourne and Cottesloe. By way of example, Mount Claremont is about eight kilometres from the Central Business District, has a median house price of about \$1.4m, the average age is 44 and the crime rate is 465 crimes per 100,000 population against a WA rate of 1,977. Within the Postcode, many of the streets are peaceful and shady and there is a mix of coastal bushland and parks such as Allen Park. There is a strong sense of community and desire to retain the status quo of a relatively idyllic environment. There is keen interest in the protection of the local environment and flora and fauna.

7. A close relationship exists between SASR and their families, and the local communities. The SASR, and Defence more broadly, has developed an excellent reputation in the area over many years. The unit is highly regarded and has been proudly adopted by the local communities around Swanbourne. The SASR contributes to the economy of the area and Defence families living in the Village are seen as important contributors to the social fabric of the broader community. They participate in local sporting and social activities and their children attend the local schools and the Child Care Centres. The community is very protective of SASR and identifies with it.

8. The Village is currently owned by DHA; however, a Deed of Covenant (the Covenant) between Defence and DHA prohibits leasing of the houses to the private sector and the development or sale of the land. The Covenant is particular to the Village '...while Defence maintains the Special Air Service Regiment (SASR) or similar special forces unit and continues to use the Special Training Facilities at Swanbourne...<sup>3</sup> The Covenant was put in place to ensure that the Village and nexus with SASR was recognised in the way DHA managed the Village. The arrangement purposely prevents DHA from applying their business model to this housing stock for operational reasons. A copy of the Covenant is at Annex A.

9. The *Defence Housing Australia Act 1987 (DHA Act)* (Reference A) clearly provides direction to DHA regarding its core responsibility. It states (in part):

'The main function of DHA is to provide adequate and suitable housing for, and housing-related services to:

<sup>&</sup>lt;sup>2</sup> Submission 83

<sup>&</sup>lt;sup>3</sup> Deed of Covenant dated 4 June 2001

## 14

# a. members of the Defence Force and their families;

... in order to meet the operational needs of the Defence Force and the requirements of the Department.'

Regardless of constraints imposed on DHA i.e. the Covenant and its responsibilities as a Government Business Enterprise (GBE), first and foremost is its duty to provide adequate and suitable housing for the ADF, including in Seaward Village.

10. Over the years various options have been discussed between DHA and Defence regarding the management of the Village and in that time the quality of the housing stock has progressively deteriorated. Currently 43 houses do not comply with agreed standards. This includes eight unoccupied due to maintenance requirements. In early 2014, Defence and DHA agreed that the Village should be redeveloped. Despite previous considerations as to why the land should not be sold, it was agreed that DHA would develop a concept proposal to sell about 25% of the Village for construction of up to 140 private houses. The proceeds from this would be utilised for building new SRs, increasing the total number from 153 to 165.

11. The redevelopment proposal met with unforeseen and considerable opposition from many stakeholders that include: the City of Nedlands Council, the Australian Special Air Service Association (ASASA), Friends of Allen Park (FOAP), Friends of Allen Park Bushland Group (FOAPBG), Sayer Street Residents, Swanbourne Coastal Alliance Inc (SCA), a number of the Village residents and the broader WA community. The stakeholders were well coordinated and their messaging was aligned and focused. In addition at least four prominent politicians, State and Federal, openly stated their concerns regarding the proposal. The issue had relatively high levels of reporting in the WA media. The *West Australian* newspaper, local media and other newspapers and state television have shown interest in the story as it developed. They appear supportive of stakeholder arguments opposed to redevelopment, centred around:

- A perceived lack of rigour in planning leading to logic gaps in the proposal
- A perceived lack of consultation, collaboration and communication
- Cynicism and lack of confidence regarding the motives and future strategy of DHA
- Impact on operational capability, SASR personnel and their families
- Selling of 25% of the land at the Village for 140 private homes
- Concern regarding the demolition of a whole Village of relatively modern houses
- Preference for refurbishment rather than redevelopment
- Prolonged construction of SRs and civilian houses (possibly concurrent to the planned Campbell Barracks Redevelopment)
- Increased traffic, particularly in Sayer Street, and its flow on impact to the surrounding suburbs

#### FOUO

• Damage to a pristine and delicate coastal environment

12. There is no doubt that within WA, substantial damage has occurred to the reputation and brand of DHA, and to a lesser degree that of Defence, as a result of the perceived weaknesses in the redevelopment concept; and the overall management and strategic communication of the project.

13. In November 2015, as a result of the very negative reaction by stakeholder groups to the proposed redevelopment, the Assistant Minister for Defence, the Hon Darren Chester, requested Lieutenant General Mark Evans AO, DSC to conduct a Review to 'evaluate the proposal for redevelopment in terms of its effectiveness in delivering quality, long term and sustainable housing for ADF members and their families, and to advise if there are any alternative options that may deliver a similar or superior outcome'. The Terms of Reference (TOR) for the Review are included earlier in this report. The Review has interpreted the TOR as requiring that a recommendation be made for an option over other options.

14. At the commencement of the Review Lieutenant General Evans was provided a small team to assist, consisting of:

- Group Captain Kathleen Powell, an Air Force Reserve officer with extensive experience in inquiries and administration, including postings in personnel management areas that dealt with ADF housing issues
- Mr Alan McClelland, seconded from Estate and Infrastructure Group Department of Defence where he is Director Relocations and Housing, responsible for managing contracts for the delivery of housing, removal and relocation services to Defence. He provided subject matter expertise on those services to the Review
- Captain Edward Scarr, an Army Reserve officer whose expertise rests in research of complex issues

# METHODOLOGY

15. The TOR were released on 26 November 2015 following a public announcement and media release by the Assistant Minister. The following timeline and methodology was applied to the conduct of the Review:

- 26 November 2015 9 January 2016:
  - Consultation and Research
  - Widespread advice of the Review and call for submissions by 15 January 2016 through media advertisements on 8 and 12 December 2015
  - Release of a DEFGRAM on 10 December 2015
- 10 15 January 2016:
  - Visit to Perth including two visits to Seaward Village
  - Meetings with key stakeholders

# • 16 January 2016 – 9 February 2016:

- Consolidation of information
- Confirmation of key issues with key stakeholders
- o Legal Review
- Review of DHA costings

# • 10 - 24 February 2016:

- Review of DHA costing
- Development of written report

# • 25 February 2016:

• Presentation of the report to the Assistant Minister

# BACKGROUND

16. Over the past 10 years Defence and DHA have engaged in ongoing discussions to consider options for improving the quality of houses in the Village. The options have taken into account the current standard of the houses and the cost to DHA of maintaining the properties.

17. Seaward Village was originally transferred from Defence to DHA ownership in 1992. It currently contains 153 homes, with 43 requiring major upgrade or replacement by 2017 to comply with Defence minimum housing standards. The remaining 110 houses are compliant but require upgrades. The Village is not old by community standards.

18. In June 2001 the Covenant was established prohibiting DHA from leasing or selling properties to civilians while SASR remained at Swanbourne. Over several years, DHA sought removal of this to allow the houses and land to be sold in accordance with its business model, under the sale and leaseback program. On each occasion, Defence re-affirmed the need to retain the Covenant to ensure long-term Defence housing adjacent to Campbell Barracks, commensurate with the operational requirements of SASR.

19. During the period 1992 to 2010, DHA undertook regular maintenance of the properties and carried out minor upgrades to some houses. However, the minor upgrade program was not completed because the Covenant, from a DHA perspective, made it uneconomical to invest in the properties. This has caused a significant variation in the standard of housing in the Village.

20. In November 2010, a Joint Defence and DHA Working Party (JWP) examined a range of housing issues, including rationalisation of the housing ownership arrangements between Defence and DHA and the future ownership of land and houses at the Village. The JWP report (Reference B) reaffirmed the continued importance of the Village in the provision of housing for SASR; identified that the houses were below the standard provided to Defence personnel in other areas; and recommended that DHA upgrade them to a satisfactory standard. It also recommended that if Defence was unable to lift the Covenant, other options for management should be investigated. This was to include an examination of the

17

feasibility of transferring Defence off-base properties to DHA in exchange for the land in the Village. Defence re-affirmed the need to retain the Covenant.

21. Over the next three years Defence and DHA jointly considered several options that included:

- A DHA proposal to completely redevelop the Village. This would provide additional housing for ADF members posted to Campbell and Irwin Barracks. To partially fund the proposal, DHA asked that Defence land at Irwin Barracks be excised and transferred to DHA. However, the land sought by DHA was not surplus to Defence requirements because of the planned disposal of Leeuwin Barracks and the relocation of units to Irwin Barracks.
- **Replacement of 153 existing properties with 242 new houses**. To fund this, DHA proposed that Defence approve the partial lifting of the Covenant to allow 83 of the 242 housing lots to be sold under the sale and leaseback program. At the end of the leaseback period, 159 houses would remain under DHA ownership. This proposal was further developed in late 2013 and became the basis for the final agreement between Defence and DHA.
- A proposed transfer between Defence and DHA of off-base annuity properties and the Village. This transfer was consistent with the recommendations of Reference B. During consideration of this proposal, the Department of Finance and Deregulation raised a number of concerns with land transfer/swap in relation to Commonwealth guidelines and policies; and advised it would need to be progressed through Government under the Budget Process Operational Rules. Given the complexity of Government processes and likely substantial delays in implementation, the proposal was not progressed.
- A DHA proposal to upgrade the properties with Defence contributing to the cost. The Defence preference was for DHA to fully fund the upgrade. However; to progress the proposal it took into account the restrictions of the Covenant and DHA advice that it was uneconomical to upgrade the houses. If this option was progressed, it was agreed at the working level that the Defence contribution would not exceed 50% of the total estimated cost.

22. On 11 February 2014, the Secretary and Chief of the Defence Force (CDF) met with the Chairman DHA to discuss the DHA proposal for future housing development at the Village. At this time DHA:

• Acknowledged the houses in the Village were 'in a poor state and need to be upgraded or replaced as a matter of urgency.... There is an obligation to have this work completed by 2017, the deadline nominated by Defence in 2006 for all housing stock to meet its minimum standard.'<sup>4</sup>

<sup>&</sup>lt;sup>4</sup> This comment was first raised with Defence in a letter from Chairman DHA to Secretary of Defence dated 23 August 2013.

- Advised Defence 'with the Covenant in place, DHA is not in a position to make the level of investment required to upgrade Seaward Village without assistance from Defence.'<sup>5</sup> The ageing condition of the properties and infrastructure made them commercially unviable to repair or upgrade with the Covenant in place.
- s47(1)(b) commercially valuable information
- Advised that the proposed redevelopment, partially funded by the sell-off of about 25% of the land to the public, was commercially viable and the preferred DHA option. With income from the sell-off, construction of approximately 163 new SRs could be fully funded by DHA.
- s47(1)(b) commercially valuable information which was slightly more than the cost of upgrading the existing houses. However, the advantage of the proposed redevelopment, partially funded by the sale of lots to the public, was that new, larger houses with much reduced maintenance costs would be provided on smaller blocks, ensuring a longer-term solution than the upgrade option.

In view of the foregoing, DHA sought agreement for the lifting of the Covenant to allow it to proceed with full redevelopment of the site and partial sale of the land to fund the redevelopment.

23. On 5 March 2014, the Secretary and CDF co-signed a letter to the DHA Chairman, Mr Volker, agreeing the redevelopment proposal and the preparation of a joint ministerial submission to the Assistant Minister for Defence the Hon Stuart Robert, outlining the way forward.<sup>6</sup> In the Joint Ministerial Submission dated 27 March 2014, Defence and DHA informed the Assistant Minister for Defence that Defence and DHA mutually agreed the proposed redevelopment and gave in-principle agreement to the partial lifting of the Covenant. A written brief was forwarded to the Assistant Minister outlining the proposal.<sup>7</sup>

24. On 10 November 2014, a joint Defence and DHA Ministerial Submission provided a mutually agreed way forward for the redevelopment, including an updated draft Concept Plan. The key agreed outcomes were:

- Defence would seek approval for the transfer of three blocks of Defenceowned land, adjacent to the Village, under Section 60 of the *DHA Act*
- DHA would construct 165 new three and four bedroom dwellings for Defence families

<sup>&</sup>lt;sup>5</sup> Ibid.

<sup>&</sup>lt;sup>6</sup> Letter SEC/OUT/2014/66 CDF/OUT/2014 201 dated 5 March 2014

<sup>&</sup>lt;sup>7</sup> Ministerial Advice Robert:MA14-000996 dated 27 March 2014

## 19

- There was in-principle agreement to the partial lifting of the Covenant on the land to allow redevelopment to occur and the sale of about 25% of the site area
- Civilian lots for sale to the general public would be in an area clearly separated from Campbell Barracks and the Village
- Fencing along the boundary between Defence houses and proposed civilian lots would provide a security barrier should isolation of the Defence area be necessary
- DHA would provide a replacement Child Care Centre, allowing continuity of business to prevent disruption to families
- DHA would continue to allocate existing houses to Defence families up until an agreed time
- The proposal was subject to satisfactory financing and cash flow arrangements

25. On 13 March 2015, the Assistant Minister for Defence wrote to Defence and Army senior officials outlining the key principles that were to guide the redevelopment<sup>8</sup> as follows:

- About 25% of the land could be sold to fund the redevelopment, and the sale must meet Army's security requirements
- A rolling one-stage development would allow families to stay within the Village
- An increase in the number of available houses, with a range of different property types, would give residents more choice depending on their personal circumstances
- Large backyards would remain a feature
- There would be separate entry roads to the redeveloped Village. One for Defence residents and one for those living in the 25% sold off portion
- Allocation of existing houses to new families would cease at a date mutually agreed by Army and DHA, with remaining families able to stay during the redevelopment, noting they may have to move within the Village precinct
- The Child Care Centre would operate continuously, with the old closing on Friday and the new opening on Monday to ensure minimal disruption
- Newly posted families to SASR would be housed in close proximity to Campbell Barracks (ideally no more than 10km away), with any extra costs for increased rent ceilings approved at public expense

<sup>&</sup>lt;sup>8</sup> AMINDEF/OUT/2015/019 dated 13 March 2015

# 20

# DHA REDEVELOPMENT PROPOSAL

## General

26. DHA provided a submission to the Review regarding the redevelopment proposal: *DHA Submission – Seaward Village Review* dated 15 January 2016 (Annex B). Costings for the proposed redevelopment are contained in Annexes C, D and E and are discussed later in this report.

27. DHA owns the properties and manages the Village as part of its Defence housing portfolio and over the period 2016 - 2022 plans to redevelop the site to provide modern homes for ADF members and their families posted to Perth. The redevelopment concept involves the phased demolition of the existing homes, delivering 165 modern homes along with new streets, parkland areas and a new childcare facility.

28. To assist in funding the project, the Government, Secretary of the Department of Defence and CDF agreed that DHA could sell a portion of the total site area to the public. The sale of developed housing lots to the private market would partly offset the significant cost of the redevelopment, with the balance to be funded by DHA. A major consideration in this course of action was that the development would be totally funded by DHA, with no call on Defence or Government funding.

29. The proposal to redevelop the Village that was presented to key decision makers focused on the end state and the bottom line. There is no evidence that alternatives to redevelopment were fully explored or presented, nor were the risks to this course of action identified or exposed. Surprisingly, a complete survey of the housing stock in the Village was not conducted prior to the development of the proposal. The underpinnings to the proposal, on the evidence presented, do not appear comprehensive.

# **Proposed Redevelopment Concept**

30. DHA proposed the construction of up to 145 detached houses and 20 townhouses (165 total), providing a mix of double and single storey, three and four bedroom homes, to take advantage of modern sustainability features. DHA would maximise the number of homes built to the '*Silver*' level of the '*Liveable Housing Guidelines*.'<sup>9</sup> This allows easier access for occupants with disabilities or injuries and is '*fitted for but not with*' bathroom features that enable easy modification. This feature is not in existing houses but is being included in the majority of new DHA houses across Australia.

31. The redevelopment project was designed to improve the housing standard for ADF families in the Village by bringing the quality and size of homes into line with contemporary standards and quality that DHA provides elsewhere. DHA would

<sup>&</sup>lt;sup>9</sup> http://liveablehousingaustralia.org.au/library/help/Liveable\_Housing\_Design\_Guidelines\_Web1.pdf

also undertake significant works to improve the parks and recreation areas within the site.

32. As part of the redevelopment concept, approximately 141 new lots would be created in addition to 165 houses for ADF families. These would be sold on the private market and construction would be the responsibility of the buyer. The purchasers would be bound by design guidelines to ensure all future development on this land would be in keeping with the local ambiance while maintaining the privacy of the Defence community.

33. WA Planning Commission guidelines require the site to have two access points for emergency access and evacuation. Seaward Avenue and Sayer Street would continue to be the access points. After consultation with stakeholders, DHA redesigned the layout to maximise the number of vehicles using Seaward Avenue, thus reducing the impact on Sayer Street. Other access options were considered unfeasible due to a range of factors.

34. Further redevelopment concept plans have been developed by DHA after consultation with Defence, Army and other stakeholders. DHA has also been working to bring the concept to fruition by collaborating with the WA State Government and the City of Nedlands Council. A detailed plan has still to be provided for approval by Defence and Army.

# **Undertakings to Seaward Village Residents**

35. In accordance with Ministerial guidance, DHA provided an undertaking that ADF members and their families who reside in the Village when construction commenced would have two options:

- Remain during the construction period, with a possible move within the Village during this time
- Move out of the Village and occupy a suitable house within a reasonable distance of the base, with the option of returning at the completion of the redevelopment

# 22

# Breakdown of redeveloped Seaward Village Areas

36. The following tables outline the percentage of the total areas dedicated for each proposed use:

| Existing                          |           |       |
|-----------------------------------|-----------|-------|
| Land Use                          | Area (m2) | %     |
| Public Open Space                 | 27,838    | 15.48 |
| (POS)                             |           |       |
| Road reserves                     | 45,953    | 25.54 |
| Residential                       | 103,184   | 57.37 |
| Child Care                        | 2,897     | 1.61  |
| Commonwealth (inc. Melon Hill)    | 32,353    | N/A   |
| Total (less<br>Commonwealth land) | 179872    | 100   |

| Concept                          |           |       |
|----------------------------------|-----------|-------|
| Land Use                         | Area (m2) | %     |
| DHA Lots                         | 71,809    | 35.89 |
| Civilian                         | 51,250    | 25.6  |
| Childcare                        | 2,134     | 1.06  |
| POS                              | 26,147    | 13.06 |
| Commonwealth/Melon<br>Hill       | 12,092    | N/A   |
| Public Access Way &<br>Emergency | 931       | 0.47  |
| Roads                            | 47,862    | 23.92 |
| Total                            | 200133    | 100   |

# Land Use Observations

- 37.
- The following observations are provided on this information:
  - In the redevelopment, Commonwealth land (including Melon Hill) reduces from 32,353 to 12,092 m2 and the difference (20,262 m2) is included in the figure for the land to be sold to the public
  - 41.6% of the residential land is being made available for civilian lots. The calculation to determine 'about 25% of the land' for sale has used all land in the Village (including roads, the Child Care Centre, etc) as its basis. This calculation has been a contentious issue for many stakeholders

#### FOUO

- 23
- There has been a 30% reduction in the land allocated for DHA owned housing even though there are 12 additional properties
- There has been a reduction in the amount of land provided for the POS and the Child Care Centre

# Proposed Program

38. The proposal for redevelopment is a multi-year, phased project, with anticipated timeframes as follows:

| Date             | Activity   |
|------------------|--|
| Mid 2016         | Construction of new Child Care Centre begins (including demolition of a small number of homes) |
| Early – mid 2017 | Existing Child Care Centre closes. New Centre complete and operational                         |
| Early – mid 2017 | Phased demolition and construction of new homes begins   |
| Late 2019        | First new Defence homes complete<br>Phased construction of new homes continues                 |
| 2019 - 2023      | Sale of 141 lots to the public   |
| 2022             | Redevelopment of all 165 DHA homes complete  |

DHA has ceased work on the redevelopment option; therefore, it is unlikely that this timeline will be achieved.

# Advantages

39. The proposed redevelopment, partially funded by a sell-off of lots to the public, has the advantage that new, quality, larger houses with reduced maintenance costs would provide a long term housing solution for ADF members and their families. Other key benefits envisaged by DHA were:

- Existing drainage infrastructure would be removed and replaced with underground storm water storage
- The new houses would be purpose built for the environment and increase asset value for DHA
- A long term housing solution would be delivered at a lower overall cost, at no additional cost to Defence other than an increased rental cost

# Disadvantages

40. The following disadvantages of the redevelopment proposal were identified in submissions to the Review:

- The sale of about 25% of the Village and of significant 'Defence' Land, primarily bushland, for property development, with adverse impacts on local flora and fauna
- Potential impact on SASR operational activities and training
- A reduction in security for families

# FOUO-

#### 24

- Disruption to ADF families, including the potential need for them to move, with consequences for spouse employment and children having to change schools
- The duration of the project beyond six years
- Smaller gardens for the SRs; a reduction in the amount of public open space and parkland in the Village and destruction of three memorial parks named after deceased SASR soldiers: Baines, Harris and Jones
- Increased traffic flow, particularly in Sayer Street

# **Approval Process Risks**

41. Agreement by Defence, DHA and the Federal Government is not an assurance that the proposed redevelopment will proceed. It remains subject to WA statutory planning approval processes. The project cannot proceed until the WA Government transfers state owned land to DHA. While DHA has applied for this land transfer, the application is currently not being progressed by the Department of Lands because of opposition to the project. The City of Nedlands Council, which has formed a Seaward Village Working Group that clearly opposes the redevelopment, will also be involved.

42. The Review notes that DHA is seeking to establish a broader planning framework via an Improvement Plan/Improvement Scheme process administered by the WA Planning Commission. This scheme is reserved for significant and complex projects and the proposed redevelopment has been accepted by the WA Planning Commission as such, due to the unique nature of the site, including:

- Urban design layout driven by Defence security requirements
- Complex zoning and land ownership issues
- The proposed road and open space relocation processes
- Requirement for timely management of the approval process

# **KEY ISSUES ARISING FROM REDEVELOPMENT**

# **Stakeholder Engagement**

43. The Seaward Village Review was broadly publicised to ensure that those who wished to express a view had the opportunity to do so. Advertisements were placed in *The Australian* and *West Australian* newspapers on 8 and 12 December 2015. The advertisement was also sent to WA local community newspapers. Within Defence, a DEFGRAM was distributed on 10 December 2015. The general public and Defence members were invited to make submissions by 15 January 2016.

44. In accordance with the TOR, consultation took place with Defence, DHA, the State Government, the local Council, the ASASA, Seaward Village residents, the FOAP, FOAPBG, the neighbouring civilian community and other parties that had a direct and legitimate interest in the redevelopment proposal. Any additional

# 25

stakeholders identified by Defence, DHA and the Assistant Minister's office were contacted, many of whom made a submission to the Review.

45. As noted earlier, the concept of redevelopment and partial sale of the Village was opposed by numerous stakeholder groups and individuals. While it is not unusual for there to be resistance to large projects such as this, generally attitudes soften over time after the benefits of the project become more widely recognised and accepted. This has not been the case in this instance. Resistance has strengthened and the basis for criticism has become more informed.

46. A visit to Perth was conducted during the week 11 - 15 January 2016, as part of the information gathering process and for the purpose of seeing the Village and hearing the views of residents, ADF members and other interest groups and individuals. Consultation with relevant WA Government Departments and the City of Nedlands Council Seaward Village Working Group was also arranged.

47. There was some cynicism about the timing and short duration of the Review, over Christmas and New Year during a stand down leave period for the SASR and when many in the community were said to be on holidays. Despite this, SASR and various interest groups managed to arrange meetings to inform the Review process. While ADF members and their families and most community members saw the visit in a positive light, SCA and City of Nedlands Council questioned the impartiality of the Review. Notwithstanding, all key stakeholders provided submissions within the advised timeframe.

- 48. The program for the visit included the following:
  - A DHA liaison day: inspection of the Village and examples of other DHA housing in the area, and discussions about the proposed redevelopment
  - Inspection of a range of houses in the Village
  - Meeting with Minister Julie Bishop and the Hon Andrew Hastie
  - Meeting with Senator Dean Smith
  - Discussions with ADF members and their families at the Village (approx 50 attendees)
  - Meetings with the Commissioner, WA Planning Commission and his staff and WA Department of Lands staff
  - Meeting with the National Chairman, ASASA
  - Tour of Melon Hill with SCA representatives and community members (approx 30 attendees)
  - Tour of Sayer Street and meeting with Sayer Street residents (approx 15 attendees)
  - Meeting with the City of Nedlands Council Seaward Village Working Group



FOUO-

- 26
- Meeting at Allen Park Tennis Club, arranged by FOAP, attended by various community interest groups (approx 100 attendees)

## Submissions to the Review

49. In addition to the DHA submissions previously mentioned, the Review received 84 submissions from groups and individuals. Six of the 84 made a supplementary submission. Without exception, they all opposed the redevelopment proposal. The submissions are included separately at Annex F.<sup>10</sup>

- 50. In particular, the Review received submissions from:
  - The Hon Colin Barnett, WA Premier and local member for Cottesloe:
    - Indicating support for SAS families, who favour a less disruptive refurbishment program and hold concerns about the impact on security if there was a mix of civilian and Defence homes in the Village
    - Acknowledging the scope for some higher density housing (apartments and town houses) for Defence couples without children and single members
    - Conveying the concerns of local residents and environmental groups over the loss of local bush land and increased traffic, and
    - Noting the Nedlands Council motion to close Sayer Street
  - A retired former SASR commanding officer (CO) and Commander SF, who expressed concern about the impact on security (both to Campbell Barracks and ADF families in the Village). He believes greater consideration should be given to the potential for increased security threat to families and the barracks. He also envisaged further limitations to essential training arising from noise complaints from civilians who purchase the proposed new housing
  - A retired former SASR CO who opposed the plan on security and social impact grounds, stressing the importance of the support mechanisms available to families by virtue of them residing in the Village. In his experience, housing in the Village was a significant retention factor for SASR
  - The City of Nedlands Council that believes '... most of the community opposition to the proposed redevelopment would evaporate if the sale of private lots was removed from the proposal.'<sup>11</sup> The Council:
    - o Objects to the DHA redevelopment plan
    - Considers a '*normal*' process should have been followed, involving a Scheme Amendment to the Town Planning Scheme followed by a Development Application
    - Requests formal input by the City in the decision making process

<sup>&</sup>lt;sup>10</sup> The information at Annex F has been collected without express consent being given to the public disclosure of personal information and it should be managed in accordance with Australian Privacy Principles under the *Privacy Act 1988* 

<sup>&</sup>lt;sup>11</sup> Submission 25

- 27
- Seaward Village residents who are concerned about poor DHA communication, reduction in the size of back yards and the possibility of two storey houses. They support the refurbishment option and have concerns about the social impact of redeveloping the Village
- The Chairman of the ASASA, who believes DHA profit is the foremost consideration in the proposal and that redevelopment will impact adversely on security, operational and training requirements for SASR.
- Former ADF members who believe the Covenant must remain, security is an issue with the proposed plan and refurbishment is a better option
- The SCA was critical of the timing of the Review, said insufficient time would be given to submissions and that DHA would have a disproportionate input and influence. The lack of impartiality of the Review was also questioned. SCA believes the redevelopment will impose a completely unacceptable impact on the bushland and amenity of the Allen Park precinct
- The FOAPBG has worked for 17 years on restoration of the Park (named after a Gallipoli veteran, John Allen), which is extensively used by the community. They believe the proposal for demolition of houses in the Village is unacceptable and note refurbishment allows retention of streetscapes and topography. They also expressed concern that the three parks within the village named after deceased soldiers would be destroyed
- Two Architects, one of whom sought a meeting to present a new concept for the redevelopment and another who was critical of urban design aspects of the DHA plan and proposed an alternative plan
- A Practising Valuer, who questioned the redevelopment when refurbishment was a cheaper and better option
- A suitably qualified person who focused on traffic issues and impacts, also citing other proposed developments in the area, the cumulative effect of which would have an adverse impact

51. The remainder of submissions came from local residents and community groups. The issues raised are summarised below:

# • In relation to DHA:

- the business model appeared to have taken priority over other important factors
- the plan was ill conceived and poorly developed
- the cost benefit of the proposed redevelopment was questioned and seen as unnecessary and wasteful
- the Child Care Centre had recently been upgraded and a new Centre was now proposed
- there has been poor strategic communication and a lack of consultation and sensitivity

# • In relation to Seaward Village houses:

- the need for improvement in the houses was acknowledged
- o the need for quality, long term sustainable housing was agreed
- o the rationale for demolishing the Village was questioned
- o a complete survey of the existing houses was considered necessary

## • ADF members and their families in Seaward Village:

- will face considerable disruption if required to vacate houses during the redevelopment
- are concerned about the future of the Village and this has impacted adversely on morale
- have concerns about security and also fear the loss of the Village as a respite location and supportive environment for families during deployment
- distrust DHA and fear they will not be able to return to the Village if they vacate for a lengthy period
- the current level of maintenance of the homes is poor and some believe DHA has allowed the houses to degrade by doing minimal maintenance
- DHA is receiving full rent for the houses and therefore should continue to maintain them

## • Community concerns

- o empathy with SASR regarding family disruption
- o security issues
- impact on local schools if the Village is unoccupied for a number of years
- o impact on parkland on Melon Hill, Allen Park and surrounds
- o loss of Memorial Parks in Seaward Village
- o traffic problems, Sayer Street in particular
- environmental matters, impact on pristine areas and the habitat for the Carnaby's Black Cockatoos

#### Petition

52. In addition to individual submissions, an online Petition: '*Protect Seaward Village and Save Allen Park*,' arranged by FOAP, was endorsed by 575 supporters. Overall, the views expressed in the Petition reflect concerns for the security and welfare of Defence families, environmental concerns, planning issues and loss of local amenity.

#### Summary

53. In summary, numerous important issues have been raised by various stakeholders that have potential to impact on the successful outcome of this project to varying degrees. They range from the existing Covenant; the merits of redevelopment; linkage to SASR capability, i.e. security, encroachment and noise, and social issues; through to the environment, traffic, and strategic communication. As noted earlier,

#### FOI 198/20/21 Report

#### FOUO

## 29

other than submissions from DHA, no submissions were received in support of the proposed redevelopment.

# The Covenant

54. In 1992, Defence (acting for the Commonwealth) transferred to DHA its interest in land at the Village. In 2001, Defence and DHA entered into an unregistered Deed of Covenant in which DHA undertook:

"... that while Defence maintains the Special Air Service Regiment ("SASR") or some similar special forces unit and continues to use the Special Training Facilities at Swanbourne, DHA will not:

1.1 lease any house in the estate into the private sector without the consent of the Minister for Defence; or

1.2 deal with or encumber or sell any of the houses or undeveloped parts of the land into the private sector.'

55. Since its introduction, the Covenant has been an effective method of ensuring property in the Village is retained for the exclusive use of housing ADF members and their families, as originally intended. However, as the redevelopment proposal has been agreed and requires that DHA sell about 25% of the land on the private market, a variation or replacement of the Covenant is now required.

56. In order to achieve this, Defence and DHA must mutually agree to either vary the terms of the current Covenant or terminate it and establish a new one. The second course of action is preferred as the Covenant can be updated and expanded to include undeveloped Defence land being transferred to DHA at no cost. It could also include arrangements for the Child Care Centre.

57. Defence has confirmed that a new Covenant would be established on the properties retained in DHA ownership for use by ADF members and their families. This would place similar restrictions on the sale and leasing of properties as the current version.

58. DHA has agreed to establish a restriction on the Title of the land it sells to civilians to ensure the Security Principles advised to DHA by Defence are implemented. Defence has sought specific details of the measures being proposed by DHA to ensure its requirements are being met.<sup>12</sup>

<sup>&</sup>lt;sup>12</sup> Director Relocations and Housing email to COO DHA dated 1 February 2016

# The Nexus with SASR

# General

59. Fundamental to the proposal for redevelopment should have been consideration of the interconnectedness of the Village to Campbell Barracks that creates a 'Campbell Barracks – Seaward Village Zone'.<sup>13</sup>

60. Since its raising, the home base for SASR has been Campbell Barracks. The Village was initially developed as 'on base' housing to accommodate their families. Over time the housing policy has evolved and the SRs within the Village have been made available to non-SASR personnel, principally to those who work at Irwin Barracks in Karrakatta with priority given to families with special needs. Notwithstanding, the linkage of the Village to SASR operational capability has been affirmed on numerous occasions. During the Review key issues regarding the redevelopment and SASR operational capability, including morale, security, encroachment and noise, social impact and child care were examined.

# **Operational Capability**

61. SASR is a high profile unit in the Defence Order of Battle. It has gained a tremendous reputation internationally, domestically and within Defence for its professionalism and effectiveness as a SF unit. It is likely that future national security challenges are to be characterised by continuous and increasingly non-linear threats below the threshold of accepted military operations. SASR, along with a number of other agencies beyond Defence, is likely to be at the forefront of activities that will counter such threats. The current high tempo of the unit is, if anything, more likely to increase rather than decrease.

62. Reinforcing the importance of the SF capability has been the decision by Government to enhance Campbell Barracks facilities to a capital cost of \$223.6m. This will provide SASR with functional and flexible purpose built facilities and improved infrastructure; enabling SASR to maintain and develop its operational capability efficiently and effectively. The decision reinforces the strategic and operational importance of the base into the future.

63. Notwithstanding the broader utility of the Village to the Defence Community in WA, SASR tenants are the priority and its close proximity to Campbell Barracks creates an obvious nexus with the SF capability. It provides the SASR with homes for the core of its members with dependants that are close to its workplace and amenities; and privacy and security in a peaceful and quiet environment that is affordable in an expensive housing market. The importance of the contribution to capability was identified in Reference B:

'SASR is arguably the most operationally active unit in the ADF and a high percentage of its members are deployed at any one time. Housing at Seaward Village is an important part of the support provided to the families of SASR members.'

<sup>&</sup>lt;sup>13</sup> Submission 83

The redevelopment of the Village has proven to be a distraction to members of a unit experiencing a very high operational tempo, largely due to the angst it has caused amongst their families.

# Security

64. Nearly 30% of the submissions received raised the issue of diminished security as a result of the redevelopment, either relating to operational capability at Campbell Barracks and/or residents of the Village.

65. During the period May - July 2015 the Defence Security and Vetting Service (DS&VS) facilitated a Security Risk Assessment for Campbell Barracks. This portion of the security review was sought to assist Army consideration of the DHA proposal for redevelopment. Observations made by DS&VS were:

'The Village reflects similarities to a gated community, and although the public can access the roads the lack of through traffic limits the frequency of non-resident traffic resulting in a greater prospect of residents identifying activity that is out of the ordinary or unusual ... the existing layout and community has fostered a strong perception of safety and security to those in the community and those who enter the community. The current arrangements personify many of the principles of Crime Prevention Through Environmental Design (CPTED).'

66. Discussions with residents and families confirmed a strong sense of security with the current Village configuration. Families on the whole perceived that they were safe. Deployed personnel take comfort that their families are in the Village community. In their view, the redevelopment diminishes this sense of security.

67. The point of contact for the DS&VS review agreed that given the encroachment of civilian housing upon the Village there would be a diminution to the perceived level of security by residents of the Village. However, the risk assessment concluded the actual residual security risks for both Campbell Barracks and the Village, as a result of redevelopment, did not exceed risk tolerance levels for Defence Establishments across Australia. This security review was subsequently endorsed by Army.

68. At the request of Army, DS&VS developed a series of recommended security design principles. These design principles were based on accepted CPTED theory for the redevelopment. Army approved the principles and sought assurance from DHA that they would be applied in totality to the planning and execution of the redevelopment. DHA has subsequently stated they do not anticipate any impediments to the full application of the security design principles and sought permission to proceed with the redevelopment work as previously agreed. Army recently sought further information from DHA to allow the redevelopment plans to be fully considered and approved. Although security concerns regarding the proposed redevelopment have been raised by current tenants, they should not, of themselves, prevent the project from going ahead if the redevelopment complies with the design

#### FOUO

32

principles and Army requirements. Notwithstanding, there will be an impact on security as a result of the redevelopment.

## **Encroachment and Noise**

69. Campbell Barracks Redevelopment will mean that SASR is likely to remain in Swanbourne for many years to come. Its current location does not provide it with the benefits of residing within a larger secure military base as is the case with SF units of other nations, in terms of providing a buffer from civilian communities when conducting operational activities. However, its geographic position currently provides some characteristics of this necessary buffer: to the north of the Barracks is the beach coastal reserve of City Beach, further enhanced by the close training area and field ranges; to the east is Bold Park and the Cottesloe Golf Club, combined with the eastern berm along the two lane West Coast Highway; to the west the Indian Ocean with a fence line along the complete length of the barracks; and to the South is Seaward Village, currently occupied exclusively by ADF personnel and their families.

70. A high level of training activity occurs within Campbell Barracks throughout the year determined by the training cycle and operational imperatives of the unit. The characteristics of the unit require continuous 24 hour operational and mobility training that includes significant helicopter operations. The range complexes are significant and sophisticated and constant use of all types of munitions and explosives by day and night are necessary for the unit to maintain its operational edge. This creates a noisy environment that can affect neighbouring areas.

71. In order to provide noise management controls for on base ranges and to minimise disruption to surrounding areas, a self imposed curfew period currently exists and has done so for around 20 years. This means that in accordance with Unit Range Standing Orders, live firing (without weapon suppressors) and use of explosives can occur between 0600 - 2100 hours. Live firing and training that might generate excess noise can be granted by the CO outside of these timings in exceptional circumstances. Notices to the public are raised as required, giving warnings about excessive noise associated with training.

72. Service families who reside in close proximity to operational bases are accustomed to the impacts of operational noise and activity. Future encroachment of civilian housing into the buffer zone of the Village will inevitably create pressure for SASR to curtail or adjust operational and training activities; and potentially will require Defence to manage compensation claims under the *Defence Force Regulations 1952*. This issue is of concern.

# Social Impact in SASR

73. Broader social impacts are discussed elsewhere in this report; however, there have been social impacts particular to the Village residents. The redevelopment proposal has created significant worry and anxiety for families, for a number of reasons evident in the report and in the submissions received. These were reinforced during the visit to Perth. ADF members and their spouses advised they were satisfied with the existing accommodation and surrounds while acknowledging the need for the houses to be refurbished. They sought to avoid the significant disruption that the

# 33

redevelopment option would cause. This concern has overflowed to create disquiet. Some spouses said that issues surrounding redevelopment are likely to have an impact on whether their partners remain in the ADF. A SASR soldier advised that the redevelopment had impacted on the wellbeing of his family and this may cause him to separate from the Army. (His own reaction to redevelopment centred on potential risks to training.) It is clear that the issue has had an effect on unit morale.

74. A former CO reasonably summed up the social implications for the unit in his submission:

'However it is the social impact on the families that is to me just as real a concern for the future of the SAS capability. By accident of history and geography, we have a location in Seaward village which allows families to meet those expectations despite the extreme pressures that SAS military service entails. The location provides access to a life style that plays no small part in the retention rate at SASR, despite the demands and dangers of SASR service.'

And:

'While COSASR, I was left with no doubt that few soldiers ever want to leave SASR, but instead separation is nearly always prompted by partners who tire of the absences, danger...but provision of an environment for families that compensates the extreme demands on wives ... was an essential factor. In this there was no doubt that the location and environment of Seaward Village factored greatly, followed, in my assessment, by the sense of "family" it facilitated in the wives and especially during times of tragedy, so often the case on either operations or training at the Regiment.<sup>14</sup>

# Child Care

75. The Defence Child Care program is managed by the Defence Community Organisation (DCO) and provides services and support to ADF families. The Sunny Child Care Centre, located on Seaward Ave, Swanbourne is one of the Centres in the Defence program. It has a licensed capacity for 47 children per day.

76. In mid April 2015 representatives of DHA met with the DCO staff to discuss a concept for rehousing the Child Care Centre as part of the redevelopment. On completion, the children would transfer to the new centre and the old centre would be demolished. The redevelopment would meet the current level of licensing.

77. There is no evidence that the existing Child Care centre is unsuitable. Therefore, if the proposed redevelopment does not proceed, there is no need to replace the Centre. Similarly, child care issues do not prevent the redevelopment.

<sup>&</sup>lt;sup>14</sup> Submission 82

# Summary

78. All military organisations will ultimately carry out the direction of their commanders and this is the case with SASR regarding the proposed redevelopment. Irrespective of this, and despite the fact that a DHA Perth Housing Survey Report of September 2015 (Reference D) reported *'that of 61 respondents in SV (sic), 59% supported a redevelopment to some degree, 20% were against it to some degree and 21% were neutral or had no opinion,'* redevelopment has caused disquiet. There is no doubt that the current decision to rebuild and sell some of the land at the Village has created considerable concern and distraction amongst members of the unit and their families that does not appear to be reflected in the Survey. One submission addressed the issue of the Survey:

'The fundamental flaws of the survey are that:

1. It never disclosed that the redevelopment would result in a land sale of approximately 50% of the current housing area. This is a serious omission at best or a dishonest and manipulative tactic at worst;

2. It never offered any other option, such as renovating homes. This is, again, a significant omission; and

3. The survey was long, lacked clarity, and was cleverly written to give DHA the results they wanted, rather than to provide them with an accurate representation of members' opinions.<sup>15</sup>,

79. During the visit to Perth at a meeting with approximately 50 Village residents on 13 January 2016, there was a unanimous indication that a refurbishment option was preferred. It was clear from discussions with soldiers and their families that the redevelopment had become more than just an irritant, that it had impacted on morale and was likely to affect retention in the unit.

80. The ASASA submission included the following:

'Ahead of all other considerations, the current sound buffer zone around Campbell Barracks must be preserved to safeguard SASR's training and operational requirements. The loss of that buffer on SASR's operations readiness will be significant and could in a short time bring into question the future suitability of Campbell Barrack as a base for SASR. Secondly, there are a range of security issues to be considered including physical security measures to preserve the safety and security of families. These can only be ignored at the peril of the decision makers. And lastly, there are a range of morale related issues that could arise if families are forced to relocate from the Village, and these could well have major implications for SASR manning and its operational effectiveness into the future.<sup>16</sup>

<sup>&</sup>lt;sup>15</sup> Submission 22A

<sup>&</sup>lt;sup>16</sup> Submission 71

35

81. The redevelopment proposal brings with it a number of complexities that do not appear to have been given due consideration. Whatever concept for improving the Village is selected there remains a clear nexus between the Village and the SF capability. Significant weight should be placed on maintaining the integrity of a high end operational capability through consideration of the needs of Defence personnel engaged in continuous and dangerous activities, and those of their families, at a time of very high operational tempo for that particular unit.

# **Broader Community Issues**

82. People in the local community surrounding the Village enjoy a quiet coastal lifestyle and are happy with their existing relationship with Defence and Campbell Barracks. They are opposed to the redevelopment proposal. Sentiments expressed by community stakeholders are similar those of the Village residents. They consistently mentioned their satisfaction with the existing relationship with SASR and the Village residents. There is strong local opposition to the proposed redevelopment that is primarily focused on the disruption to ADF families, adverse impacts on the local environment and Allen Park and the increased flow of traffic into Sayer Street and the surrounding neighborhood. Various elements of the broader community place different emphasis on each issue but they appear interconnected, well informed and coherent.

# Environment

83. Of the submissions received, 25% cited environmental issues as a reason for their opposition to the redevelopment proposal. In addition, 575 people signed an on-line Petition to save Seaward Village and Allen Park. The FOAPBG submission provided background in relation to the historical significance of this park 'for *Recreation...and Natural Gardens and a Lookout...for the people...for all time.*'<sup>17</sup> Since the creation of the Park, much grant money and community effort has been expended in preserving and improving the area which is a now a valued community recreation facility.

84. Another submission described Allen Park as the 'hub' of the area, 'a total of approximately 18 hectares consisting of eight hectares of recreational space and eight hectares of bushland reserve. It is often described as the "lungs of Swanbourne." The tree canopy of peppermints and rare, aged tuart trees among coastal bushland supports wildlife, flocks of owls and the endangered Carnaby's Black Cockatoo as well as providing highly valued "mental space for humans."" Many local residents support the following view expressed in this submission: 'the redevelopment proposal has made poorly researched assumptions about the availability of community land which, if used, will have a long lasting and detrimental effect on the whole Allen Park Precinct.'<sup>18</sup>

<sup>&</sup>lt;sup>17</sup> Submission 18

<sup>&</sup>lt;sup>18</sup> Submission 8

## 36

85. It should be noted that the DHA proposal does not intend to reduce the size of Allen Park and some residents have made the assumption that Defence owned land adjacent to the Village is part of Allen Park. Informed stakeholders understood the difference and proposed that this Defence land, including Melon Hill, should be incorporated into Allen Park.

86. DHA commissioned an environmental study of the Village area, with a Flora and Fauna Survey competed in late 2015. The study did not identify any issues that would prevent the redevelopment from proceeding. DHA advise that a detailed assessment of the environmental requirements will be made by relevant authorities as part of the planning process and they will comply with all State and Federal Environmental legislation. DHA has undertaken a detailed Bushfire Risk Assessment and the site is classified as a bushfire prone area, hence the importance of the two access/egress points in the existing Village and for any redevelopment. On the available advice, there is no long term environmental reason to prevent the progression of this option.

# Traffic

87. The WA Planning Department Bush Fire Management Guidelines require that any Seaward Village redevelopment have two separate access routes for emergency access and evacuation. At present, access to the Village is gained primarily through Seaward Avenue, with Sayer Street providing secondary access. The redevelopment proposal would see no change to this existing access network although there will be an increase in the flow of traffic on Sayer Street.

88. DHA-commissioned independent modelling indicates that, under the current proposal, traffic along Sayer Street will increase from 230 to 724 vehicles per day. In the morning peak hour, it is anticipated that 60 vehicles would use Sayer Street (equating to approximately one vehicle per minute). This is below the design limit of this street which planning guidelines advise could cope with 3,000 vehicles per day. DHA has investigated other access roads. These include:

- A public access road through Campbell Barracks, an option not supported by Defence. Because it runs parallel to Seaward Avenue it does not provide a viable alternative route
- A road south through Allen Park, connecting to Odern Crescent. Initial advice to DHA is that this would not be supported by the City of Nedlands Council

While residents have a contra view, DHA advice is that the existing road network has the design capacity to accommodate the projected traffic volume increase and the issue of traffic on Sayer Street would not, of itself, prevent the redevelopment from going ahead as planned.

89. The residents of Sayer Street and the City of Nedlands Council object to the ongoing use of Sayer Street as a point of access/egress to the Village and say they intend to close and remove the portion of Sayer Street that traverses the existing A-Class reserve. They propose a track with *'knock down bollards'* that would be

#### FOUO

#### 37

available for emergency use only. Several submissions addressed this point. One stated: [the DHA] '...planning path is to use an existing road, Sayer Street as the primary ingress and egress for the proposed development. Part of the route that runs from Seaward Village into Sayer Street is an A Class Reserve which DHA is proposing to breach.' This would 'cause much public antagonism in the future, because of the environmental damage and loss of habitat to endangered species along with a very detrimental traffic impact on the local civilian community. That antagonism will most likely, albeit incorrectly, be directed towards the Department of Defence and Campbell Barracks instead of towards DHA....'.<sup>19</sup>

90. DHA advice is that Sayer Street is the most appropriate secondary access route, both for Seaward Village residents and the wider Swanbourne community. That Sayer Street crosses an A-Class reserve, a fact cited by the City of Nedlands Council, does not provide a basis for its closure and non-use as an access/egress route. Public roads through A-Class reserves are not uncommon in WA, the most notable examples being roads that run through Kings Park and John Forrest National Park.

91. The closure of Sayer Street not only represents a significant risk to the viability of the current proposal, it also represents an increased risk to the safety of residents in the Village irrespective of the option finally chosen. A replacement access/egress point would need to be identified before Sayer Street is closed. The WA Department of Lands advises that providing a track with *'knock down bollards'* is not an adequate solution. The Minister for Lands in the WA Government is the delegate for resolving this matter. As such it is beyond the scope of this Review.

#### Risks

92. A decision to proceed with the current proposal has the following identified risks:

- The proposal has floundered in its execution, possibly due to poor coordination and communication and a perceived lack of collaboration at the outset. This has polarised attitudes in the community. Continuing with redevelopment will likely trigger a very active anti-redevelopment campaign that will further damage the reputation of Defence and DHA.
- The proposed redevelopment remains subject to the relevant WA statutory planning approvals and transfer of State-owned land. The WA Premier, in his capacity as the State local member, has expressed his opposition to the current proposal.<sup>20</sup> Currently, the processing of issues has stalled and the required approval may not be given.
- It will have a deleterious impact on the morale of members and families that has potential to impinge on retention and operational capability.
- Encroachment on capability noise from the training on Campbell Barracks will predictably be an irritant to owners of the private blocks which, over time, may corrode the ability of SASR to conduct required

<sup>&</sup>lt;sup>19</sup> Submission 8

<sup>&</sup>lt;sup>20</sup> Submission 10

FOI 198/20/21 Report

FOUO

38

training. This has already occurred with the imposition of a 0600 - 2100 hours noise curfew on range practices.

• Sayer Street is currently used as the second entry/exit point to the Village. Local resistance may prevent this from remaining, in which case an alternative would need to be found. No viable alternatives have been identified to date.

## A FEASIBLE ALTERNATIVE - REFURBISHMENT

93. The TOR required that feasible alternatives to redevelopment be explored. Essentially three options were identified based on achieving distinct outcomes; they are: redevelop, refurbish or disposal. The disposal option (disposing of the Village from DHA housing stock and selling the land), has been considered and determined to be inconsistent with the strategic decision to redevelop Campbell Barracks. Other than the agreed proposal of redevelopment, the only other identified feasible alterative is refurbishment. A refurbishment process looks to renovate or improve existing buildings through an upgrade program. The program can add additional amenities and rooms to the building; replace old appliances, fixtures and fittings and generally improve the house. In circumstances like the Village the refurbishment is done through a rolling program with a limited number of houses off line at any one time, causing less disruption to families. In this case, one obvious difference between the redevelopment and refurbishment models is the manner in which they are funded. Funding options are discussed later in this report.

94. In this section of the report, the term *'refurbishment'* is used to indicate work to enhance the quality of the existing property although it is not a contractual term prescribed in the *Services Agreement on Housing and Related Matters* (the Services Agreement)<sup>21</sup>. In that document, the term *'upgrade'* is used. In this report *'refurbishment'* and *'upgrade'* have a common meaning that allows for the inclusion of new or improved amenities.

- 95. The Services Agreement contains the following definitions:
  - Upgrade means either a Major or Minor Upgrade
  - **Major Upgrade** means, in relation to a SR, a major improvement in quality, amenity or standard, including the addition of a significant amenity (such as an extra bedroom or ensuite) or when a SR requires midlife upgrade due to being aged or run down
  - **Minor Upgrade** means, in relation to a SR, a minor improvement in quality or standard, such as a new bathroom fit-out or new kitchen fit-out
  - In the Services Agreement, there is a clear distinction between an upgrade and repair and maintenance

<sup>&</sup>lt;sup>21</sup> The Services Agreement is the Defence arms length commercial arrangement with DHA that is the basis for the delivery of housing to meet Defence needs. Its contract terms prescribe housing standards, service levels and performance requirements. It also sets the basis for payments by Defence to DHA for housing

39

• **Maintenance** means to keep in good condition through renewal or repair of decay, defective or worn-out parts for premises and the fixture and fittings (excluding the tenants' fixtures and fittings) and does not extend to expenditure of a capital nature

Often, failure to pay attention to repair and maintenance can generate the requirement for refurbishment.

#### **Refurbishing DHA Houses**

96. The DHA business model generally involves replacing leased houses on the Rent  $Bill^{22}$  before they require Minor or Major Upgrades. It relies on construction, sale and leaseback of houses and the direct leasing of properties. Under Department of Finance GBE guidelines, a principal objective is that any activity should add to shareholder value. Although in keeping with its responsibilities under the *DHA Act* and the Services Agreement, refurbishing leased housing stock rarely provides a commercial return.

97. When houses are retained in DHA ownership (i.e. DHA-owned houses) because they are strategically located to meet Defence requirements or have been purchased for a specific purpose, refurbishment occurs when required but not normally in significant numbers or as large projects. The replacement of older houses with new houses on a new site is the preferred option. This is consistent with the DHA business model and permitted by the Services Agreement. Generally, DHA does not demolish houses to replace them on the same site unless there are opportunities to redevelop more than one property and increase the yield by providing additional houses (i.e. demolish three properties to provide seven new homes).

98. The most recent large project to refurbish DHA-owned houses occurred in 2006 when DHA carried out a Major Upgrade of 150 houses at Wattle Grove (adjacent to Holsworthy Barracks). This project went very well and Defence identified no significant issues.

99. In recent years, projects to improve the standard of Defence-owned houses on bases and in remote areas have generally involved the upgrading of houses rather than replacement. This strategy was selected as substantial improvements can be achieved at reduced costs per house and with more reasonable options for tenant management in remote areas or on bases. These projects have occurred at Larrakeyah, RAAF Tindal, *HMAS Cerberus* and Puckapunyal. In most instances, the cost of a Major Upgrade is less than half the cost of constructing new houses and the refurbished houses delivered to Defence by DHA are consistently of a high standard.

100. However, in a few instances (e.g. RAAF Darwin and Canungra), the cost of refurbishing older houses was similar to providing new houses. In those instances, Defence chose to have new houses constructed.

<sup>&</sup>lt;sup>22</sup> The Rent Bill is the monthly invoice through which all payments related to SRs are made. There is a formal process for including houses on the Rent Bill

#### 40

#### Suitability of Seaward Village Housing for Refurbishment

101. In 2011, DHA advised that 43 houses did not comply with the 2007 Defence policy minimum standard and would be classified as transitional stock and require substantial renovation, primarily by the inclusion of an ensuite, or demolition and reconstruction by 2017. The remaining 110 were compliant but many required a mid-life upgrade, while 33 had been recently upgraded and needed minor refurbishment. In 2012, DHA advised that the cost of upgrading the properties at the Village was estimated at <sup>\$47</sup> During discussions on the possibility of transferring ownership of the Village to Defence, it was agreed that few, if any, of the houses would need to be demolished and replaced. DHA cost estimates for refurbishment have grown by 122% since then.

102. During the visit to Perth, the first impression on driving through the Village is of an attractive and well-established suburban area. The housing area is quiet, relatively isolated, well maintained, and obviously well regarded by the inhabitants. There is substantial tree coverage throughout public areas and on most properties which enhances the attractiveness of the Village. The houses are older than normal DHA houses; and, in particular, the living areas are smaller than what is now normal in modern houses. However, overall the houses appear to be of sound standard, consistent with those in the surrounding areas. The size of the housing allotments is much larger than DHA provides elsewhere. The overall appearance of the Village was adversely affected by vacant houses with gardens in need of care.

103. Of the houses inspected, three were in good condition. One was occupied and required no additional work. Two had been vacated in recent months and required standard post-vacation maintenance, such as repainting of walls and ceilings before being reoccupied. Three other houses were in obvious need of attention and required an upgrade such as refurbishing kitchens and bathrooms, new floor coverings, curtains and fittings. Another house was older, did not comply with current Defence minimum standards and required the addition of an ensuite. This was in poorer condition than the remainder and required a major upgrade. The roof leaked and there was damage to the ceilings and walls. A large retaining wall on the downhill side of the property was collapsing and needed repair.

104. One criticism of the redevelopment option raised by stakeholders is the waste of resources associated with the demolition of 153 twenty-year old houses when most could be retained for many years. They argue that the suburb of Swanbourne comprises houses that are a similar age and standard. The claim that all houses in the Village are poor quality and not up to Defence standards was not substantiated during the visit to the site. Most of the houses had not reached their economic life span.

105. It was apparent that the condition of some of the houses has deteriorated over time, with some requiring significant work to upgrade to a suitable standard. This decline is most apparent in the 43 houses constructed before 1991. An assessment is now required to determine whether some need to be replaced. From the information made available during the visit, most of the houses are suitable for upgrading.

#### 41

106. DHA advised that, since the decision to redevelop the village was agreed, tenants have received the same level of routine maintenance provided to ADF families around Australia. Current maintenance is directed at meeting the needs of the tenants of occupied houses and maintaining the condition of the houses. However, this view is not shared by tenants and the standard of maintenance was a consistently strong criticism of DHA raised by tenants. Maintenance of unoccupied houses has been limited to security and grounds maintenance. As agreed between Defence and DHA, no new allocation of the Village housing has occurred since July 2015.

## s47(1)(b) - commercially valuable information

108. DHA has advised that its estimated cost is robust and includes contingency allocations (15%) to cater for unexpected issues that could occur. Accordingly, this estimate could be considered a maximum figure for the refurbishment program. However, if houses need to be replaced because it is uneconomical to upgrade them, the cost of the new houses should be identified separately.

109. Once a thorough assessment is done of each property and a firm quote becomes available, the financial risks with an upgrade program are low. Unlike the rebuild option, the final net cost is not dependent on fluctuations in the volatile Perth property market.

110. As part of the current redevelopment, DHA is addressing several issues associated with the Village infrastructure, particularly the management of storm water. It is noted that DHA has not conducted any detailed analysis on drainage infrastructure. If this is a critical issue, it would also need to be addressed as part of the refurbishment program and project costs may need to be adjusted. However, information provided to the Review suggests that current storm water management arrangements are adequate for the existing houses as the inundation of lower park areas has a negligible impact because of the sandy soil in the Village.

#### **Evaluation of the Refurbishment Option**

#### Advantages

111. The refurbishment option has the following advantages:

#### 42

- **Cost.** The cost of this option is significantly less than the net cost of redevelopment and on a *'like with like'*<sup>23</sup> basis, i.e. building costs, refurbishment of the Village would be less than half the cost of redevelopment. The cost could be spread over a period of up to five years and would provide a continuing rent stream for at least 100 houses throughout the project
- **Best use of current assets.** Most of the houses are about 20 years old and their condition does not warrant demolition and replacement
- **Time.** The project would be quick to plan and implement. Work could commence shortly after the first tranche of houses has been assessed and while later tranches are being surveyed. There are about 40 houses currently vacant (as at 6 January 2016) and these could be used for the first round of upgrades, for delivery in late 2016
- **Disruption to Tenants.** This option minimises the level of disruption to ADF tenants. While tenants would need to change houses as the project progressed, the level of inconvenience and complaint would be manageable because families would be moving to better quality home in the same area
- **Retains the ADF Village.** Most stakeholders want to retain the Village as an ADF enclave.
- Limits encroachment on Campbell Barracks. No civilian families would be located in the valley that is affected by noise from Campbell Barracks
- Limiting the footprint of the Village. The concerns of non-ADF interest groups, such as the FOAP, would be alleviated as the footprint of the Village would remain unchanged with no additional impact on the surrounding environment
- **High quality of upgraded housing.** DHA has a strong track record of providing high quality results from upgrading programs

#### Disadvantages

112. The upgrade option has the following disadvantages:

- More expensive. On a net cost basis this option is potentially fiscally more expensive
- **Reversal of a decision**. This would be a reversal of a decision agreed by Government and the senior leadership of Defence and DHA
- **Resources committed**. Resources have been committed to progress the agreed redevelopment of the Village. Should the refurbishment option be adopted most of the investment to date would be lost

<sup>&</sup>lt;sup>23</sup> Enclosure 1

#### FOUO-

- 43
- **Precedent**. Reversal of the redevelopment decision due, in part, to community pressure may establish a precedent, though the Village is a unique case

113. In summary, the refurbishment of Seaward Village provides a sensible way forward that makes best use of existing housing. If this option is chosen, there are three available models for funding the project.

#### Model 1 - DHA Fund Upgrade

114. This model recognises that the Village properties are owned by DHA and should be maintained to the standard prescribed in the Services Agreement.

115. The Covenant reflects an undertaking provided by DHA when the Village land was transferred from Defence to DHA. This undertaking was advised to the Public Works Committee (PWC) in April 1991. DHA endorsed the Covenant and should have been aware that this included responsibility for some form of minor and major upgrading programs in due course. The circumstances have not changed since then, apart from a substantial increase in SASR operational tempo and an even greater need for housing in the Village for their families. This has previously been recognised by DHA and two limited programs to refurbish the properties were commenced but not completed because DHA decided not to continue the work.

116. DHA retains ownership of about 2500 investment properties nationally and maintains and upgrades them in accordance with risk sharing arrangements prescribed in the Services Agreement. While the Covenant makes the Village a unique case, the contract obligation to maintain the properties continues to apply. Given that DHA has projects worth over \$1b currently underway, the cost of an upgrade program for the Village, spread over five years, is unlikely to significantly affect other DHA activities and operations. DHA could seek Shareholder Ministers' agreement to adjust its annual dividend payments to meet the cost if required.

- 117. Model 1 has the following advantages:
  - It is consistent with DHA obligations as prescribed in the *DHA Act* and risk sharing arrangements set out in the Services Agreement
  - The cost of an upgrade program for Seaward Village, spread over five years, is unlikely to affect other DHA activities and operations

118. The disadvantage of Model 1 is the solution continues to require DHA to operate within the constraints of the Covenant. The cost of upgrading and replacing houses is generally recovered through increased capital value of the house, that cannot be realised with the Covenant, and additional rent.

#### Model 2 – Shared Cost

119. Following the decision not to progress the exchange of off-base annuity properties and the Village, Defence and DHA staff commenced an investigation into Defence partially funding the upgrade program. As the basis for the investigation, it

#### 44

was agreed at the working-level that the Defence contribution would not exceed 50% of the total estimated cost.

120. At that time, Defence indicated its preference for DHA to fully fund the refurbishment (Model 1). However, Defence recognised that for a solution to be found the constraints of the Covenant needed to be given full consideration

121. The model provided a pragmatic solution to this longstanding and contentious issue. However, the investigation was overtaken by events and was not completed, although it was clear the net costs would be significantly lower for DHA and Defence than the other models.

122. To be successful, this model, like all alternatives, must not only address the current requirements but also establish clear guidelines for future upgrade programs. These arrangements should be formalised in the Services Agreement. One issue that would need to be addressed is the level of funding Defence would provide when houses are unsuitable for upgrade and need to be replaced.

- 123. This model has the following advantage:
  - It provides a pragmatic, compromise solution that may be acceptable to both Defence and DHA
- 124. It has the following disadvantages:
  - It would generate costs for Defence
  - The model is inconsistent with existing Services Agreement risk sharing arrangements and specific contract arrangements would need to be agreed for the Village
  - The level of Defence funding for replacement housing would need to be determined

#### Model 3 – Ownership Transfer

125. As discussed in the Background, in 2010 the JWP examined a range of housing issues, including the future ownership of land and houses in the Village. It recommended that, if Defence was unwilling to lift the Covenant and it was not economically viable for DHA to maintain the properties to Defence standards, other options should be investigated. This was to include an examination of the feasibility of transferring Defence off-base properties to DHA in exchange for the land in the Village.

126. If a transfer was to occur, it could be undertaken quite expeditiously and with little administrative effort on either side. There are three potential transfer options:

• Option 1. DHA transfer Seaward Village properties to Defence at no cost. As a government entity, DHA is responsive to its Shareholder Ministers and it could be directed by the Defence Minister to return the

#### FOUO-

#### 45

properties to Defence under the *DHA Act* S.31(2), with the agreement of the Minister for Finance. Essentially, DHA would gift the land to Defence

• Option 2. DHA transfer Seaward Village properties to Defence at an agreed price (perhaps book or market value) and Defence liability could be calculated as an annuity. Alternatively, Defence could fully pay the agreed price.<sup>24</sup> The Services Agreement defines an annuity as follows:

'Annuity means an agreement between Defence and DHA to amortise the costs relating to acquiring, constructing, upgrading, holding and/or financing a Service Residence over a fixed term in accordance with Schedule 3 (Annuities).'

 Option 3. DHA trade the Seaward Village with Defence for property of equivalent value. s47G - business affairs

127.

The advantages of the transfer option are:

- It would enable the Village to be recognised as part of the '*Campbell Barracks* Seaward Village Zone' and its contribution to operational capability, layered security, and prevention of encroachment would be assured
- The transfer of ownership to Defence would be supported by tenants and local community groups as it would retain the status quo and avoid the sale of lots to the public

## s47(1)(b) - commercially valuable information

- It clarifies responsibilities and brings the Village into line with other Services Agreement risk sharing arrangements and provides a clear, longterm solution for maintenance, refurbishment and replacement
- Defence retains the Village for continuing use by the ADF in a location where all housing is expensive and difficult to provide

128. The disadvantage of this model is the transfer of the Village properties to Defence does not address the issue of the current condition of the houses. They would still require refurbishment, with costs being the responsibility of Defence. It would be the slowest model to implement, as Defence would need to seek PWC approval for the major project to proceed. This could delay the project by 12 - 24 months.

<sup>&</sup>lt;sup>24</sup> Defence may need to strike an annuity for each property for a nominal amount to ensure the requirements of the *Land Acquisitions Act 1989* are met

129. For option 3, many of the properties that could be transferred to DHA are in regional areas and are ageing, requiring upgrade or replacement in the near future. s47(1)(b) - commercially valuable information

#### Summary

130. Of all the models, it is Model 3 that will provide a long term solution to addressing the friction between the Covenant and the DHA business model.

## COST COMPARISON

131. In early December 2015, DHA was asked to provide costings for redevelopment and refurbishment to inform the Review. In addition, the Chief Finance Officer Department of Defence agreed to arrange validation of the DHA costings when they became available.

132. A DHA submission - *Project Financials Seaward Village Review* was included as a commercial-in-confidence attachment to the DHA submission to the Review dated 15 January 2016. This is at Annex C. After queries were raised in relation to this information, DHA provided a revised submission: *Revised Project Financials Seaward Village Review* dated 3 February 2016 (Annex D). On 16 February 2016, following a request from the Review for costing of a five year rolling refurbishment program, DHA provided additional information: *Seaward Village – 5 Year Refurbishment Feasibility Costing* (Annex E).<sup>25</sup>

133. The validation of DHA costings was conducted by Jones Lang LaSalle (JLL) (ACT) Pty Ltd, acting on instruction from Defence. The JLL *Valuation Critique* is at Enclosure 1.<sup>26</sup>

#### **Background Information**

- 134. DHA provided the following information regarding houses in the Village:
  - **Upgrades.** Thirty three houses underwent a minor upgrade at a cost of <sup>\$47</sup> per dwelling between November 2010 and December 2012.
  - **Rent.** DHA receives about <sup>\$47</sup> pa in rent and vacancy charges for the 153 properties.

#### **Basis for Costs - Redevelopment Option**

- 135. DHA included the following information for key cost items:
  - Civil construction costs and authority fees have been based on advice of a civil engineer

<sup>&</sup>lt;sup>25</sup> Annexes C, D and E contain commercial-in-confidence information provided by DHA

<sup>&</sup>lt;sup>26</sup> The JLL *Valuation Critique* is commercial-in-confidence and confidential to the Department of Defence

- Landscaping construction costs have been based on advice of a landscape architect
- Temporary accommodation and relocation costs have been identified by DHA in accordance with local market conditions
- Housing construction costs are based on recent tenders and quantity surveyor advice, both completed for the Perth region
- Other costs are estimated in accordance with DHA internal processes, based on experience with other development projects within its portfolio

# s47(1)(b) - commercially valuable information

#### **Refurbishment Initial Cost Estimates**

s47(1)(b) - commercially valuable information

138. As noted earlier in this report, on 15 January 2016, DHA provided detailed costs estimates for both options. Following an examination of these by the Review, DHA was asked to review the information because several areas in both options, but particularly for refurbishment, were difficult to understand. On 3 February 2016 DHA provided revised estimates s47(1)(b) - commercially valuable information

# s47(1)(b) - commercially valuable information

140. DHA was also asked to cost the refurbishment as a rolling program over a five year period. This request was made because the Review considered this was the maximum period needed to refurbish 153 houses, noting that a recently completed project to refurbish 193 houses at RAAF Tindal was completed in 3.9 years. <sup>\$47</sup>

48

s47(1)(b) - commercially valuable information

s47(1)(b) - commercially valuable information

**Basis for Costs - Refurbishment Option** 

s47(1)(b) - commercially valuable information

<sup>148.</sup> It is possible that several houses could be deemed unsuitable for refurbishment and replacement houses will be required. The number of houses to be rebuilt would be determined following the survey.

JLL Valuation Critique

s47(1)(b) - commercially valuable information

## **RELATIVE MERITS**

151. Central to this issue has been an imperative to improve housing for ADF members and their families in the Village. In consideration of the relative merits, cognisance has been given to the fact that the redevelopment of the Village was agreed by Defence and DHA. The two options of redevelopment and refurbishment have been described above. The relative merits are outlined below.

#### Redevelopment

152. This Review has confirmed that proceeding with the agreed proposal of redevelopment, is feasible. The end state will be that Defence personnel will be provided with new homes in the Village with the costs and risks shouldered by DHA. However, the achievement of this end state requires the lifting of the Covenant; the sale of at least 25% of the Village to developers; demolition of 153 brick homes; the relocation and disruption of numerous Defence families; and the rebuild of 165 SRs over a period of about six years, plus further construction of about 140 civilian homes beyond that time.

153. During the process of redevelopment, even if a decision is made to proceed, it is likely that the position of those stakeholders who are opposed to the proposal will harden and there is the possibility of a more active and coordinated campaign against redevelopment, focused on the numerous identified issues. The opposition is unlikely to go away in the short to medium term. Any action other than stopping redevelopment is unlikely to assuage the protagonists of their stance regarding: disruption to SASR operations and families; views on the false economy of the project; and impacts on the broader community including traffic and environmental issues. In addition, DHA is at the beginning of a process and has no guarantee of bringing the project to successful conclusion in its journey through State Lands and Planning Departments and Nedlands City Council processes. Also, the potential closure of Sayer Street as an egress point to the Village is unresolved.

154. If the redevelopment option is progressed, DHA will almost certainly have to 'reset' and start again with a new process of consultation, collaboration and communication. DHA will recommence the project from a low base in terms of its reputation and trust. In essence it has lost the 'hearts and minds' campaign.

#### Refurbishment

155. The alternative refurbishment option would focus beyond the bottom line and address operational capability, sustainability, and community issues more holistically. This option is feasible. It would retain the integrity of the Village as intended by the Covenant. It would not provide the same modernity and quantity of houses that the redevelopment would achieve. The homes would be upgraded to a good condition but would remain essentially 1980/90 brick homes – sound homes nonetheless and meeting the agreed standard. Deficiencies in modernity would be offset by proximity to work and amenities, and a sense of security and community.

156. The cost for refurbishment is potentially greater than the net cost of redevelopment, albeit the Village remains an asset that is intact. It is a cost that will need to be borne in some other way. This option is far less complex. Its attraction lies in part in its simplicity. It can be quick to initiate and quick wins can be achieved at a number of levels. It provides the opportunity for DHA to rebuild its brand and many of the stakeholder concerns would dissipate.

#### 51

#### Table - Comparison of Key Elements

157. The table below represents a comparison of key elements of both options:

|   | ISSUE  | REDEVELOPMENT  | REFURBISHMENT  |
|---|--|--|--|
| 1 | Agreed option                                      | Redevelopment has the agreement of Defence and DHA   | Not considered a feasible<br>option when redevelopment<br>proposed by DHA  |
| 2 | Precedent  | Not applicable   | The selection of this option<br>may establish an argument of<br>precedent for future similar<br>projects                               |
| 3 | Cost<br>comparison <sup>27</sup>                   | s47(1)(b) - commercia  | ally valuable information  |
| 4 | Building Costs                                     |  |  |
| 5 | Land ownership                                     | Sale of at least 25% of land<br>on the open market   | No land sale. The integrity of<br>the Village is maintained.<br>There is an option of<br>transferring the land to<br>Defence ownership |
| 6 | Operational<br>Capability                          | Impacts on layered security<br>provided by the Campbell<br>Barracks-Seaward Village<br>zone                            | No encroachment of civilian<br>housing<br>No change to security profile  |
|   |  | Encroachment of civilian<br>housing into the noise<br>buffer zone with potential<br>effects to operational<br>training | Noise buffer zone intact<br>No impact on operational<br>training regime  |
| 7 | Impact on morale<br>of ADF members<br>and families | Disruption and uncertainty<br>for ADF member families.<br>Adverse impact on morale                                     | Concerns redressed. Some disruption but easily manageable  |
| 8 | Demolition of<br>Properties                        | Demolition of Estate of<br>153 houses of which most<br>are current occupied  | Replacement of some houses<br>may be required  |
| 9 | State of housing                                   | New homes  | Refurbished homes that meet the agreed standards   |

# s47(1)(b) - commercially valuable information

#### 52

|    | ISSUE                                  | REDEVELOPMENT   | REFURBISHMENT  |
|----|--|---|--|
| 10 | Number of houses                       | Increase of 12 homes  | No planned increase  |
| 11 | Overall<br>stakeholder<br>satisfaction | Concerns of stakeholders<br>not addressed. Anti-<br>redevelop campaign<br>continues   | Most stakeholders have<br>achieved their desired<br>outcome, less Sayer Street<br>residents          |
| 12 | Additional<br>community<br>concerns    | Community concerns<br>regarding traffic and<br>environment will need<br>continual management  | Except for the issue of the<br>closure of Sayer Street most<br>other issues would be resolved        |
| 13 | Timeframe<br>comparison                | Six year project that is<br>phased. Construction of<br>civilian homes will go<br>beyond that period   | Refurbishment could be<br>completed over a five year<br>period as a rolling program                  |
| 14 | Planning approval<br>processes         | No guarantee that<br>proceeding with this option<br>will result in a successful<br>conclusion due to the<br>requirement to negotiate<br>with WA Planning and<br>Land Departments and<br>opposition from the City of<br>Nedlands Council | No significant planning<br>processes are required  |
| 15 | Housing<br>availability                | The Village will provide<br>limited accommodation<br>during the redevelopment   | Most houses would remain<br>available, indeed some<br>currently vacant houses could<br>be reoccupied |
| 16 | Income flow                            | Rental income ceases for<br>the majority of homes<br>during demolition  | Income flow from rent is<br>maintained during<br>refurbishment                                       |
| 17 | DHA brand                              | Seriously impacted in WA  | Opportunity to rebuild brand and reputation  |

#### Summary

158. The redevelopment project has struggled largely because its merit has been unable to be sold to key stakeholders. There appear to be logic gaps in the reasons for the redevelopment and the conclusion has been drawn, rightly or wrongly, that the DHA business model has been the driver in this initiative; rather than the need to improve the homes for ADF families in the Village in a more comprehensive way.

159. Refurbishment, while probably more expensive in dollar terms, will not impact on operational capability, it will utilise extant housing and allay the fears and address the concerns of Village residents, the broader community and other key stakeholders. It would achieve a satisfactory accommodation outcome that would alleviate disruption to a unit and families exposed to a high operational tempo. Its merit lies in part in its simplicity and its minimisation of risk.

#### 53

## CONCLUSION

160. The story of Seaward Village and the redevelopment proposal is underpinned by the need to provide quality, long term and sustainable housing for ADF members.

161. The history of the Village has been punctuated by milestones of affirmation of the importance of its relationship to SASR capability and the desire to retain it as an ADF housing precinct albeit owned by DHA. The establishment of the Covenant in 2001, agreed by Defence and DHA, was a direct result of this intent.

162. The Covenant created a unique model for Defence and DHA to manage. It purposely placed a constraint on DHA that limited its management options. In essence this was part of doing business with Defence. It was not intended that they could apply their business model in this instance to provide 'adequate and suitable housing.' Notwithstanding, it created a significant tension for DHA in terms of its main function directed in the *DHA Act* and its requirement to act as a GBE. This is a significant issue that rests outside the TOR but needs addressing in due course.

163. The plan for redevelopment of the Village appears to have been driven by a desire to apply the DHA business model. There appears to have been a reluctance to invest in improving the Village to any great extent indicated by the cessation of a refurbishment program that was under way in 2012. Certainly, a detailed and complete analysis of the state of the housing prior to the proposal being presented to Defence is not apparent, nor has any documentation been provided to confirm a thorough identification of risks. The proposal for redevelopment was attractive in terms of achieving the original aim of better housing for ADF members and families. The added attraction for Defence was the costs and risks would be borne largely by DHA.

164. It could be argued that insufficient weight or consideration was placed in the original planning done by DHA on non financial factors, such as the geography of the Village, a complete understanding of the current state of the housing stock, connection of the Village to significant operational capability, its position and relationship to communities inside the City of Nedlands, or possible reactions to a redevelopment proposal from key stakeholders.

165. This Review has considered the merits of the redevelopment proposal against the alternative of refurbishment. There is merit in the aspiration of producing more and newer houses in the Village for ADF personnel through redevelopment. However, since agreement to the redevelopment proposal was gained its progress has been marred by significant opposition from many stakeholders, in part due to poorly coordinated communication of intent. This opposition has become increasingly coordinated, effectively leveraging off support, at the political level, from local Government and the local media. Key issues have centred around the motivations of DHA, the efficacy of the project, the sale of land for private ownership, demolition of 153 homes, disruption to SASR operations, e.g. diminution of security, and

54

encroachment into the noise buffer zone; disruption to ADF families; environmental and traffic issues; and the perceptions of poor consultation, collaboration, coordination and communication. Along the way the reputation of DHA has been damaged, as has that of Defence, to a lesser degree.

166. Refurbishment, when compared against the net cost of redevelopment, appears to be a more expensive option, although the current costings are assumption based rather than on a complete understanding of state of the stock. In addition, the refurbishment option will not produce new modern houses but it can provide high quality houses that can be maintained in a sustainable way. This option would alleviate much of the friction that has developed and quick wins would be achieved. Overall, there are fewer risks in this option achieving an acceptable outcome.

167. The TOR requested this Review to 'evaluate the present proposal for redevelopment and its effectiveness in delivering quality, long term and sustainable housing for ADF members and their families, and to advise if there are any alternative options that may deliver a similar or superior outcome.' As indicated earlier, the options of redevelopment and refurbishment are both feasible. However, given the difficulties that have arisen during the redevelopment process this option is arguably beyond the culmination point for success. It is considered that it will continue to be bedevilled by the issues raised in this report. Fundamentally, the 'hearts and minds' campaign has been lost. Refurbishment is a more conservative approach that would achieve similar housing results i.e. a quality, long term and sustainable housing solution, although not modern homes. Importantly, refurbishment would produce a superior overall outcome.

168. On its merits refurbishment is an option that carries less complexities and less risk. Refurbishment is recommended. The paper provides three models for consideration as to how refurbishment may be taken forward. A long term solution to the issues that have brought DHA to this point would be the consideration of ownership transfer of Seaward Village from DHA to Defence. Whichever option is selected, it is important that it is acted upon expeditiously.

## RECOMMENDATIONS

169. Following a thorough review of all available information, the following recommendations are made for consideration:

- The redevelopment of Seaward Village should not proceed
- The Covenant should remain in place and the sale of land in Seaward Village should not be considered in the short to mid term
- A refurbishment program for Seaward Village should be initiated as soon as possible, designed to provide high quality refurbished houses and reduce disruption to ADF members and their families
- Consideration should be given to ownership transfer of Seaward Village from DHA to Defence in the long term
- Robust communication strategies should be developed to support the refurbishment program





## COMMONWEALTH OF AUSTRALIA

AND


## DEFENCE HOUSING AUTHORITY

## DEED OF COVENANT

0/A Awangele 822 4/12/02

DOWNINGS LEGAL SOLICITORS LEVEL 11 2 MILL STREET PERTH WA 6000

TEL: 9321 1211 REF: VKJ/JC/941116



COMMONWEALTH OF AUSTRALIA acting through the Department of Defence of care of Defence Estate Office – Perth, Leeuwin Barracks, East Fremantle, Western Australia ("Defence")

AND:

s22

DEFENCE HOUSING AUTHORITY of 26 Brisbane Avenue, Balton Authorit Capital Territory ("DHA")

#### **RECITALS**:

- A Defence is the registered proprietor of land known as Seaward Village, Swanbourne.
- B By an instrument dated 9 October 1992 the then Minister for Defence, Science and Personnel determined that part of Defence's land at Seaward Village be transferred to DHA subject to certain conditions.
- C The parties have entered into this Agreement to evidence their respective rights and obligations relating to the transfer of the agreed land to DHA, and the development and disposition of the Seaward Village land generally.

#### **DEFINITIONS:**

#### **OPERATIVE PART**

#### 1 Acknowledgment by DHA

DHA undertakes that while Defence maintains the Special Air Service Regiment ("SASR") or some similar special forces unit and continues to use the Special Training Facilities at Swanbourne DHA will not:

- 1.1 lease any house in the estate into the private sector without the consent of the Minister for Defence, whose consent will not be unreasonably withheld; or
- 1.2 deal with or encumber or sell any of the houses or undeveloped parts of the land into the private sector.

#### 2 Acknowledgment by Defence

Defence undertakes that while DHA is restricted from selling or leasing houses or other parts of the estate into the private sector pursuant to Clause 1, Defence will pay to DHA the rent set by DHA for any house in the estate for which DHA does not have an eligible tenant. 2

#### 3 Mutual Agreements

Defence agrees that if the improvements constructed on Sublot 499 are destroyed or cease to be used as a child care or Defence community facility it will transfer that Sublot 499 back to DHA free of improvements, without consideration and with no encumbrances, with each party bearing their own costs of that transfer.

Executed as a Deed.

| Signed for and on behalf of the )<br>COMMONWEALTH OF AUSTRALIA )<br>by h , Head Defence )<br>Estate being an authorised officer in )<br>the presence of: )   |       |  |              |
|--|-------|--|--------------|
| witness  |       |  |              |
| TANYA HOWE (3/5701)<br>Name<br>Department of Defence<br>Russell Offices (RA-3-119)<br>CANBERA ACT 2600<br>Address  |       |  |              |
| <u>Serior Executive Assistant</u><br>Occupation  |       |  |              |
| Signed by DEFENCE HOUSING )<br>AUTHORITY by its Attorney JOHN )<br>KENNETH MURRAY who declares that he)<br>has no notice of revocation of the Power of )<br>Attorney registered at the Office of Titles )<br>No. H62869 under which he has |       |  |              |
| executed this Deed in the presence of )<br>s22<br>Witness:   |       |  |              |
| Name: Davin Lungs Envarse<br>Address: 10 ANAGUMA COM RAPID   | MEEIC | N  | 081)         |
| Occupation: REAL ESTIMA CONSULTANT   | ۵     | DAVID L EDW<br>MISSIONER FOR (<br>PH (08) 8935 | DATHS (N.T.) |

CSIC - WA DEFENCE REGISTRY

10

32

5

Folio .....



Your ref: Our ref: 96010553/CC

30 January 2002

Mr Tony Fanowrios Defence Centre - Perth Leeuwin Barracks Locked Bag No. 5001 FREMANTLE WA 6160 **REGISTERED MAIL** 

Dear Mr Fanowrios

## Seaward Village, Swanbourne, WA - Transfer to Defence Housing Authority

We refer to our telephone conversation on 30 January 2002. 1.

We confirm that the new duplicate Certificates of Title in respect of Lot 301 on 2. Plan 22248 and Lot 499 on Plan 22245 have issued.

We enclose for safe keeping the following documents: 3.

• Certificate of Title Volume 2218 Folio 834 (Lot 301 on Plan 22248);

• Certificate of Title Volume 2218 Folio 797 (Lot 499 on Plan 22245); and

• duplicate Deed of Covenant dated 4 June 2001 between Commonwealth of Australia and Defence Housing Authority.

Could you please sign and return the attached copy of this letter confirming 4. receipt of these documents.

5. As discussed, we will shortly confirm with you that this matter has been completed and proceed to close our file.

matter na. Avenheue file \$22 #12

**Business and Commercial** 

2 The Esplanade, GPO Box U1994, Perth WA 6845 • Tel (08) 9268 1199 • DX122 East Perth • Fax (08) 9268 1771 OFFICES IN CANBERRA, SYDNEY, MELBOURNE, BRISBANE, PERTH, ADELAIDE, HOBART, DARWIN, TOWNSVILLE



## **Managing Director**

15 January 2016

Group Captain Kathleen Powell Department of Defence BP35-2-12 PO Box 7926 CANBERRA BC ACT 2610

Dear Group Captain Powell Katty

Please find attached (Attachment A) Defence Housing Australia's (DHA) submission regarding the review of the proposed redevelopment of Seaward Village, Swanbourne, Western Australia. Also attached (Attachment B) is a submission with financial information which has been separated from the main submission because the details are commercial-in-confidence and public disclosure of this information could compromise the outcome of approaches to the market that have yet to be undertaken.

We hope that DHA's submissions will assist Lieutenant General Evans in evaluating the present proposal to redevelop Seaward Village and its effectiveness in delivering quality, long-term and sustainable housing for ADF members and their families.

Please contact me on (02) 6217 8510 if Lieutenant General Evans would like to discuss any of the matters contained in the submissions.

Yours sincerely

s22

Jan Mason Acting Managing Director

Attachments:

- A. DHA Submission Seaward Village Review dated 15 January 2016.
- B. DHA Submission Project Financials, Seaward Village Review dated 15 January 2016.



26 Brisbane Ave Barton ACT 2600 dha.gov.au ABN 72 968 504 934



# **DHA Submission – Seaward Village Review**

15 January 2016

## Contents

| ABOUT DHA   | 3                |
|---|------------------|
| DHA AS A GBE<br>DHA'S BUSINESS MODEL<br>Seaward Village and the DHA Business Model<br>Arrangements Between DHA and Defence                                    | 45               |
| HOUSING AT SEAWARD VILLAGE  | 6                |
| BACKGROUND<br>COVENANT<br>FUTURE HOUSING SOLUTIONS<br>HOUSING OPTIONS CONSIDERED<br>REFURBISHMENT VS REDEVELOPMENT<br>PROGRESSION OF THE REDEVELOPMENT OPTION | 6<br>6<br>7<br>8 |
| PROGRESSING THE REDEVELOPMENT PROPOSAL  | 9                |
| STATE AND LOCAL GOVERNMENT ENGAGEMENT<br>Consultation and Communications<br>Key Issues  | . 9<br>10        |
| CONCLUSION 1  | 12               |
| ATTACHMENTS   |                  |
| 1. COMMUNICATIONS AND CONSULTATION  |                  |

## **About DHA**

DHA was established as an Australian Government Business Enterprise (GBE) under the *Defence Housing Australia Act 1987* (DHA Act). The Act states:

- 1. The main function of DHA is to provide adequate and suitable housing for, and housing-related services to:
  - a. members of the Defence Force and their families; and
  - b. officers and employees of the Department and their families; and
  - *c. persons contracted to provide goods or services to the Defence Force, and their families; and*
  - d. persons contracted to provide goods or services to the Department, and their families;

in order to meet the operational needs of the Defence Force and the requirements of the Department.

DHA is operationally located within the Department of Defence (Defence) portfolio and has two shareholder ministers, the Minister for Defence and the Minister for Finance. Responsibility for operational matters is presently delegated to the Assistant Minister for Defence.

Under a range of services agreements between DHA and the Department of Defence, DHA offers the following services to approximately 60,000 Australian Defence Force (ADF) members:

- Family housing for members with dependents (Service Residences SRs)
- Housing for single members living off-base
- Administration and management for ADF families and singles living in the private sector and receiving Rent Allowance (RA)
- Allocation of all on-base single member accommodation.

#### DHA as a GBE

As a GBE under the *Public Governance, Performance and Accountability Act 2013* (PGPA Act), DHA is required to make commercial returns and to pay commercial dividends to its shareholders. DHA needs to deliver on this requirement whilst also fulfilling its functions under the DHA Act.

GBE guidelines are issued by the Department of Finance to provide guidance to corporate Commonwealth entities under the PGPA Act. DHA must follow Commonwealth Government Business Enterprise Governance and Oversight Guidelines. A key section of the GBE<sup>1</sup> guidelines that apply to DHA is as follows:

A principal objective for each GBE is that it adds to its shareholder value. To achieve this it should:

- a. operate efficiently, that is, at minimum cost for a given scale and quality of outputs
- *b. price efficiently:* 
  - *i.* a *GBE* should set prices taking into account economic forces, including the level of demand for, and the enterprise's capacity for and cost of supplying, individual goods and services
  - *ii.* the Government may impose price conditions on GBEs providing goods and services in a monopolistic market or Community Service Obligations (CSOs). Such price conditions and CSOs, where appropriate, would be in addition to those arising from regulation by the Australian Competition and Consumer Commission and generally specified in legislation or through contractual arrangements.

<sup>&</sup>lt;sup>1</sup> Resource Management Guide No. 126, Commonwealth Government Business Enterprise Governance and Oversight Guidelines August 2015, page 3.

- *c. earn at least a commercial rate of return, given the obligations in (a) and (b) above to price and operate efficiently:* 
  - *i. This means recovering the full cost of the resources employed, including the cost of capital.*
  - *ii.* Working towards a principal financial target and a dividend policy, agreed in advance with the Shareholder Ministers, with the principal financial target to be set on the basis that each GBE should be required to earn commercial returns at least sufficient to justify the long-term retention of assets in the business, and to pay commercial dividends from those returns.

DHA is a full tax paying entity with access to a government provided debt facility. It receives neither funding nor appropriation directly from the Australian federal budget. DHA is required to maintain a strong balance sheet and to meet shareholder return obligations, including paying the government an annual dividend.

#### **DHA's Business Model**

In order to achieve its goals under the DHA Act, DHA undertakes property development and building activities across Australia, providing local jobs and hiring local contractors in the process.

Other than for Defence properties provided under annuity arrangements, Defence pays market rent (plus certain fees and charges) for all occupied houses to DHA. This represents about half of DHA's income.

Funds to meet capital requirements are sourced from the DHA property investment program and other land and property sales. Income from all sources (including rent for occupied houses) is used to supply ADF members with quality housing solutions and provide a commercial return to DHA's shareholders.

DHA also provides property and tenancy management services for DHA managed properties, which include DHA, Defence, and investor owned properties.

During 2014-15, DHA:

- acquired land to deliver approximately 3,500 allotments for future Defence housing properties
- acquired and constructed 1,154 properties
- managed 13,099 properties on behalf of investors
- generated \$498 million from property sales to investors under DHA's property investment program
- s47(1)(b) commercially valuable information
- achieved earnings before interest and tax (EBIT) of \$140 million, with net assets of \$1.5 billion
- paid its Government shareholders \$54.7 million in dividends.

The DHA model has been successfully delivering a range of housing solutions to ADF members for 25 years. A key to the success of the model has been DHA's ability to constantly replenish the property portfolio to ensure ADF members continue to have access to modern, well-maintained, well-located, and compliant (to Defence specified standards) housing.

Another key component of the success of this model is DHA's ability to act as a property developer, enabling it to control the construction of high quality housing for ADF members as well as being able to supply surplus properties for sale to the general public. Advantages of this model include:

- DHA can often acquire greenfield (undeveloped) and brownfield (industrial/commercial infill) sites more cheaply than buying completed dwellings from other developers or builders.
- Undertaking residential developments enables cost benefits arising from economies of scale, resulting in DHA delivering quality housing for ADF members at a lower cost.

• Buying large, well located sites allows DHA to positively influence the community and family environment, ensuring greater ADF tenant and investor satisfaction.

As a general rule, DHA retains approximately one third of any development for Defence housing, with the remainder being sold to the general public. The majority of the retained properties (for Defence housing purposes) are sold through DHA's property investment program, and leased back for a period, usually between 6 and 15 years, depending on Defence's likely housing need in the region.

Returns are generated from both elements of the DHA property development process. These funds are reinvested back to build and retain strategically located housing close to Defence bases in all states and territories.

DHA's property investment program has resulted in DHA leasing about 13,000 dwellings from investors. As the lease agreements approach expiry, DHA has the option to extend the lease or hand the property back to the investor. This decision is largely based on Defence needs, but is also influenced by tenant feedback on the neighbourhood and quality/liveability of the house. Returning dwellings at about 15 years of age to investors reduces long term maintenance costs to DHA, provides a manageable turnover of properties and helps to ensure quality, compliant housing for ADF members.

#### Seaward Village and the DHA Business Model

Properties that best fit the DHA model are relatively new, well-designed, well-maintained and located close to Defence establishments. Although the Seaward Village houses are well-located, they are in poor condition, having been affected by the harsh coastal climate that accelerates deterioration.

Any repair or upgrade activity must have regard to value for money considerations. Under the DHA's business model, the retention of well-located housing must be funded by the income from its development and property investment program revenue streams. DHA undertakes a stringent financial assessment for each development and upgrade project to ensure that expenditure is calculated to deliver value for money, is distributed appropriately around Australia based on Defence provisioning requirements, and is aligned with corporate objectives.

As at 31 December 2015, the 153 lots owned by DHA at Seaward Village were valued at s47(1)(b) DHA is paid market rent on occupied dwellings, with DHA's income being broadly represented by market rent plus fees and charges paid by Defence, less the cost of repairs and maintenance and other property holding costs (such as rates). In a steady state situation, without major refurbishment costs and assuming the houses are fully available and occupied, DHA's return on capital is s47 As such, this represents a s47 on the capital invested in these assets by DHA/Government.

#### Arrangements Between DHA and Defence

Defence housing policy is administered by the Defence People Group in accordance with the Australian Defence Force Pay and Conditions Manual (PACMAN). Contractual arrangements between Defence and DHA are managed by the Defence Estate and Infrastructure Group and are detailed in the Services Agreement on Housing and Related Matters (Services Agreement).

Under this agreement, DHA's Rent Bill is paid monthly by Defence. DHA does not bill ADF members directly as they are charged a standardised rent, based on their rank, across Australia by Defence. Rent payments are deducted by Defence from the ADF member's salary.

The Services Agreement allocates market and ownership risk to DHA for all areas, including Seaward Village.

## Housing at Seaward Village

#### Background

Seaward Village comprises 153 properties, built during the period 1984-94. They were transferred from Defence to DHA ownership in 1992. Of the 153 existing properties within Seward Village, 43 are not compliant with Defence's minimum standard, effective 1 July 2017. To ensure DHA does not breach its contractual obligations to Defence, the non-compliant properties require major upgrading or replacement by 2017. The remaining 110 houses are compliant but due to their poor condition require major upgrades to enable their continued use.

Whilst not old by community standards, Seaward Village houses are in poor condition, mainly due to being located in a harsh coastal environment with corrosive salt air, situated on undulating sand hills that lead to subsidence issues, as well as being surrounded by trees that cause significant root damage.

#### Covenant

In June 2001, a Deed of Covenant that prohibits DHA from leasing or selling properties to civilians while Defence retains SASR at Swanbourne was agreed between Defence and DHA.

This covenant exists to ensure long-term Defence housing is retained adjacent to Campbell Barracks, unless there is agreement otherwise between DHA and Defence.

#### **Future Housing Solutions**

In addition to the regular maintenance of properties during the period 1992 to 2010 DHA also carried out minor upgrades to many of the houses at Seaward Village. However, due to the condition of properties being worse than anticipated, there were cost blow outs and subsequently it was determined that it was uneconomical to continue investment in the upgrade program, leading to significant variations in the standard of housing within Seaward Village.

Over the past 10 years, Defence and DHA have engaged in ongoing discussions to explore options for improving the quality and standard of the houses in Seaward Village. The options have taken into account the poor condition of the houses and the high cost to DHA of maintaining the properties to the standards required by Defence.

In November 2010, a Joint Defence and DHA Working Party examined a range of housing issues between Defence and DHA including the rationalisation of the housing ownership arrangements between Defence and DHA and the future ownership of land and houses at Seaward Village.

The report identified that housing at Seaward Village was below the standard provided to ADF personnel in other areas and recommended that DHA bring the housing up to a satisfactory standard. It recommended that if Defence was unable to lift the covenant and it was not economically viable for DHA to maintain the properties to Defence standards, other options should be investigated. This was to include an examination of the feasibility of transferring Defence off-base properties to DHA in exchange for the land at Seaward Village.

#### **Housing Options Considered**

During the period 2010-13, Defence and DHA jointly considered several options in detail that included:

• A DHA proposal to completely redevelop the village to create a modern housing complex that would provide additional housing for ADF members posted to Campbell Barracks and Irwin Barracks. To partially fund the proposal DHA sought Defence land at Irwin Barracks be excised and transferred to DHA. Unfortunately, the land sought by DHA was not surplus to

Defence requirements because of the planned disposal of Leeuwin Barracks and the relocation of units to Irwin Barracks.

- The replacement of the current 153 properties with 242 new houses. To fund this, DHA proposed that Defence approve the lifting of the covenant to allow for 83 of the 242 housing lots to be sold under the sale and lease back program. At the end of the leaseback period 159 houses would remain under DHA ownership. This proposal was further developed in late 2013 and became the basis for the agreement between Defence and DHA for the current redevelopment proposal in November 2014.
- Transferring the 153 Seaward Village properties back to Defence ownership via a 'land swap' of other Defence owned off-base properties. During consideration of this proposal, it became clear that it may not be a simple swap as envisaged. Given the likely substantial delays in implementation, it was decided that the proposal would not be progressed. It should be noted that a transfer of the land to Defence would not of itself resolve the current state of repair, and that an upgrade or redevelopment would still be required.

#### **Refurbishment Vs Redevelopment**

It was determined that the advantage of the proposed redevelopment, partially funded by a sell-off of lots to the public, was that new, high quality, larger houses with greatly reduced maintenance costs would be provided, ensuring housing could remain viable and provide a longer term solution for the ADF members and their families posted to the Perth region.

The benefits of a redevelopment over a refurbishment are as follows:

- Redevelopment provides a longer term housing solution for the benefit of ADF members and families posted to the Perth location.
- The architecturally designed, larger, higher quality homes would be appropriately designed to better withstand the coastal environment, and provide greater amenity for ADF members and their families who reside there.
- The high quality parks, designed specifically with interactive equipment for Seaward Village residents of all ages, would be both more attractive and more usable.
- The poor drainage infrastructure would be removed by providing underground storm water storage.
- DHA would remove and replace street trees that were continually causing damage to driveways as well as sewer and drainage infrastructure.
- The redevelopment would fix retaining wall structural issues to avoid a potential safety hazard.
- The redevelopment would provide an additional 12 dwellings for ADF members and their families.
- The redevelopment would provide a limited number of five bedroom dwellings.
- The silver level dwellings would better accommodate injured / disabled residents.
- Through best of class urban and dwelling design, the passive surveillance of the open space areas would greatly improve personal and physical security.
- The passive surveillance measures would remove existing concealment opportunities within current open space areas.
- The new houses would be more appropriate for the area and increase the asset value for DHA.
- Families would receive a new, better designed child care centre in an improved location.
- The long term housing solution would be delivered at a lower cost to DHA and at no cost to Defence.

#### **Progression of the Redevelopment Option**

On 11 February 2014, the Secretary of Defence and Chief of the Defence Force (CDF) met with the then Chairman of DHA to discuss the DHA proposal for the future housing development for Seaward Village under the redevelopment proposal.

- Defence agreed that the ageing condition of the properties and infrastructure made them commercially unviable for DHA alone to repair or upgrade.
- DHA advised the costs of an upgrade (details of which are provided in DHA's Commercial in Confidence submission). DHA concluded that if the 153 houses were upgraded in 2015, further costly repairs would still be needed in about 10 years.
- DHA advised that the proposed redevelopment option, partially funded by the sell-off of some lots to the public, was commercially viable for DHA, and preferable to an upgrade. With the income from the sell-off, this option could be fully funded by DHA.
- s47(1)(b) commercially valuable information

The advantage of the proposed redevelopment was that new, high quality, larger houses with greatly reduced maintenance costs would be provided, ensuring a far longer term solution than the upgrade option.

On 5 March 2014, the Secretary of Defence and Chief of the Defence Force co-signed a letter to the then Chairman of DHA, agreeing to the redevelopment proposal and the preparation of a joint submission to the Assistant Minister for Defence on the way forward.

In a joint submission dated 27 March 2014, Defence and DHA informed the then Assistant Minister for Defence that Defence and DHA had mutually agreed to the proposed redevelopment of Seaward Village, and an in-principle agreement to the partial lifting of the covenant. An outline of the proposal was provided to the then Assistant Minister for Defence.

On 10 November 2014, a joint Defence and DHA submission provided a mutually agreed way forward between Defence and DHA for the redevelopment of Seaward Village, including an updated draft Concept Plan (refer Attachment 1). A summary of the key agreed outcomes is as follows:

- Defence would seek approval for the transfer small portion of isolated Defence owned land, adjacent to Seaward Village, under Section 60 of the DHA Act, at no cost to DHA.
- DHA proposed to construct 165 new three and four bedroom compliant Service Residences for ADF members and their families.
- In-principle agreement to remove the covenant on the land to allow redevelopment to occur and the sale of a portion of the total site area. This concept allowed for approximately 160 civilian lots.
- The civilian lots for sale to the general public would be in an area that is clearly separated from Campbell Barracks and Seaward Village.
- Fencing along the boundary between the Defence housing and proposed civilian lots would be fitted for, but not with, a 'security barrier' should isolation of the Defence area be necessary.
- DHA to provide a replacement childcare centre and ensure continuity of business to prevent any disruption to Defence families.
- DHA to continue to make available service residences for ADF families up until an agreed time.
- The proposal would be subject to satisfactory financing and cash flow arrangements.

On 13 March 2015, the then Assistant Minister for Defence, wrote to Defence senior officials outlining his key principles that would guide the redevelopment as follows:

- A portion of the total site area may be sold to fund the redevelopment, and this sale must meet Army's security requirements.
- A rolling one-stage development that facilitates the remaining families to stay within Seaward Village.
- An increase in the number of available houses, with a range of different property types to give residents more choice, depending on their personal circumstances.
- Large back yards continue to feature.

- Separate entry roads to the village for the military and the portion sold off to the public.
- Posting of new families into Seaward Village to cease at a logical date (to be mutually agreed between Defence and DHA) and remaining families would be able to stay during the redevelopment, noting they may need to move within the village precinct.
- The child care centre to continue to operate with the old centre to close on Friday and the new centre to open on Monday to ensure minimal disruption to families.
- Newly posted families to SASR to be housed in the closest proximity to Campbell Barracks (ideally no more than 10km away) and any extra costs due to increased rent ceilings to be approved.

Since December 2014, DHA has been progressing development plans in consultation with Defence and the various stakeholder groups. DHA and Defence established a working group in mid-2014 that has met regularly to ensure coordination and communications on all aspects of the project. This working group is attended by representatives from:

- DHA
- Defence
- Army Head Quarters
- Special Operations Command

Defence Families of Australia (DFA) has also attended a number of meetings. An outline of the current proposal and draft concept plan for the redevelopment is at Attachment 1.

#### **Cost Comparison**

DHA has provided detailed cost breakdown in a separate submission as commercial-in-confidence. If either option proceeds, the public release of detailed budgets would impede DHA's ability to achieve best value for money from its tendering processes.

#### **Progressing the Redevelopment Proposal**

#### State and Local Government Engagement

In order to mitigate project risks, DHA has commenced discussions with key local and state government stakeholders. Prior to the final agreement between DHA and Defence, on 5 September 2014, a meeting was held between DHA and executive personnel from the City of Nedlands, the Department of Planning, and Department of Lands. It was agreed that a Project Steering Group would be set up to ensure close consultation and ongoing engagement with these key approving authorities.

#### **Consultation and Communications**

Communications from Defence and DHA to all interested parties have been extensive, although initially fragmented. DHA and Defence initially agreed that Defence would take the lead in consultation with ADF members and their families, whilst DHA consulted the wider community after the information had been provided to the ADF community.

This diverse approach failed to deliver a consistent message, causing issues amongst both residents and local community groups who sometimes received different information, or the same information, at differing times. This resulted in Seaward Village residents and local community being dissatisfied with DHA over the engagement process and having ongoing trust issues.

From 1 July 2015 DHA took the lead on all communications and was able to enact its usual community engagement processes, and commenced a thorough and proactive community engagement process for the redevelopment.

A detailed summary of all stakeholder consultation activities is provided as Attachment 1.

#### Key Issues

Noting the multiple stakeholders and competing interests, the following key issues have been identified or have arisen as a result of the consultation process, and have either been addressed or are in the process of further consideration:

#### Security

Defence and local community members have raised concerns over security arrangements following a redevelopment. The security of ADF members and their families is a priority for DHA and Defence. DHA will comply with the outcomes of the Security Review.

A security review of Campbell Barracks, with consideration of the redevelopment of Seaward Village, has been conducted by Defence. DHA provided Defence with a response to the requirements of the Security Review, and does not believe the Security Review outcomes preclude a redevelopment proceeding.

The release of any Security Review documentation is a decision for the Department of Defence.

#### Traffic

DHA understands that some local residents are concerned about increased traffic movements, particularly on Sayer Street, although other roads as well.

Traffic modelling has been undertaken which shows that future traffic volumes, whilst greater than currently experienced, would be well within the Western Australian Planning Commission design limits.

An independent traffic engineering consultant has provided modelling that indicates, based on the current development proposal, traffic along Sayer Street would increase from 230 vehicles per day to 724 vehicles per day. Further analysis indicates that 60 vehicles would use Sayer Street during the morning peak hour, equating to approximately one vehicle per minute. This is well below the design limit of this street which, under planning guidelines, could handle 3,000 vehicles per day.

Following concerns raised by the local community, DHA has reconfigured the road layout to ensure Seaward Avenue becomes the primary access road for both the Defence and civilian precincts.

The Western Australian Planning Commission's Bush Fire Management Guidelines requires that a Seaward Village redevelopment have two separate access routes for emergency access and evacuation. Any closure of Sayer Street without first opening a secondary access road would not be in accordance with these guidelines.

DHA has investigated other access roads. These include:

- A public access road through Campbell Barracks. Defence has advised it would not support this.
- A road south through Allen Park, connecting to Odern Crescent. DHA has been advised this would not be supported by the City of Nedlands.

There are no other viable road access options available. Significant planning work has gone into determining that Sayer Street is the most appropriate secondary access route, both for Seaward Village residents and the wider Swanbourne community.

#### Sayer Street

Part of Sayer Street crosses an A-Class reserve. This situation is not uncommon in Western Australia. The most notable examples of this are roads that run through Kings Park and John Forrest National Park.

Sayer Street's continued use as a road is required to provide access to the local community for the Defence and civilian communities in Seaward Village. The closure of Sayer Street would force the 724 vehicles proposed to use Sayer Street to use an alternate route into the local Swanbourne community.

#### Child Care Centre

The child care centre is owned by Defence and currently operated by Mission Australia under contract to the Defence Community Organisation (DCO). DHA proposes to replace the existing Child Care Centre with a new, purpose built child care centre as a matter of priority.

The November 2014 concept plan located the child care centre located on Sayer Street in the south east corner of the site. However, feedback from residents of Seaward Village indicated a desire that the child care centre remain more centrally located, and not on the perimeter of the site. Feedback from Sayer Street residents indicated they did not want a child care centre located near their properties.

Following the consultation with Defence, Seaward Village residents, and the local community, DHA has planned to construct the new child care centre on the northern side of Seaward Avenue. This change has been well received by all stakeholders.

Should the redevelopment proceed, a seamless transfer of operation will occur for all families using this service. The old centre would close on a Friday and the new centre would open on the following Monday, minimising disruptions.

#### Environmental – Flora and Fauna

The protection of Melon Hill is of high importance for the local Swanbourne Community and, following feedback from the local community, DHA has moved the proposed development area away from Melon Hill.

The top part of Melon Hill will remain Department of Defence land and not be transferred to DHA. DHA understands the community would greatly value this land being transferred to the State of Western Australia to incorporate into Allen Park reserve.

DHA's independent expert environmental consultant has completed a flora and fauna survey, and does not believe any flora or fauna issues have been identified that would prevent a development proceeding.

Should the development proceed, a detailed assessment of the environmental requirements will be made by the relevant authorities as part of the comprehensive planning process.

DHA will comply with all state and federal environmental legislation.

#### Statutory Planning Approvals

The development requires a suite of statutory planning approvals.

DHA is seeking to establish a broader planning framework via an Improvement Plan / Improvement Scheme process that is administered by the Western Australian Planning Commission. An Improvement Plan and Improvement Scheme Process is reserved for significant and complex projects.

DHA believes Seaward Village is a significant and complex project due to the unique nature of the site including:

- Urban Design layout driven by security requirements to meet Defence needs
- Complex zoning and land ownership issues
- Road and Open Space relocation processes
- Timely management of the approval process

Local community members are concerned that if an Improvement Plan / Improvement Scheme Process occurs, they will not have the opportunity to provide input and be consulted about the development. This is not so.

As part of the Improvement Scheme process the development will go through a formal public consultation process run by the Western Australian Planning Commission. The community would have formal opportunities to comment and provide input throughout this process.

As part of the Improvement Scheme process the City of Nedlands will also have opportunity to be involved in the project steering group.

#### Covenant

Defence has agreed to removal of the covenant to facilitate the current redevelopment proposal, including that a portion of the land could be sold to raise the necessary funds to enable redevelopment to proceed.

DHA and Defence have also agreed that a covenant may be placed on the new Defence housing properties at Seaward Village.

#### **Developing the Concept Plan**

The concept plan that was the basis of the agreement between DHA and Defence in late 2014 provided for 165 houses for ADF members and their families, as well as approximately 160 lots in the civilian precinct that could be sold to the general public. DHA's concept plan options have been matured following consultation with:

- State Government Project Steering Group (DHA plus representatives from the City of Nedlands, Department of Lands, and Department of Planning)
- Friends of Allen Park
- Sayer Street residents
- Community feedback (includes all interested parties, including residents of Seaward Village)
- Defence community consultation and feedback
- Department of Defence, including the Security Review

Following the consultation process, and refinement of the concept plans, this has now reduced to 141 civilian lots. The total yield for the development is now expected to be 306 lots.

The current draft concept plan is provided at Attachment 2.

#### Conclusion

Following extensive consultation and engagement with Defence and a range of other stakeholders, including the general community, DHA commenced detailed planning for the redevelopment of Seaward Village as per the agreed concept proposal.

DHA welcomes the review by LTGEN Evans. DHA will continue to provide a high standard of housing for ADF members and their families in the Perth area and will comply with the Government's decision on the review report.

## Attachment 1

### **Communications and Consultation**

Since early 2010, DHA and Defence had been in discussions to determine a solution to what was recognised as an impending issue regarding the deteriorating quality of the housing provided at Seaward Village. In November 2010, a Joint Defence and DHA Working Party holistically examined a range of housing issues between Defence and DHA, including the future of the land and houses at Seaward Village.

The report identified that housing at Seaward Village had fallen below the standard provided to Defence personnel in other areas and recommended that DHA bring the housing up to a satisfactory standard. Over the next three years Defence and DHA jointly considered several options to do so, with the conclusion that, if any substantial improvement was to be made to the housing in Seaward Village, it had to be undertaken and funded by DHA.

On 5 March 2014, the Secretary of Defence and CDF co-signed a letter to the then Chairman of DHA agreeing the redevelopment proposal and the preparation of a joint ministerial submission to the then Assistant Minister for Defence on the way forward. In a Joint Ministerial Submission dated 27 March 2014, Defence and DHA informed the then Assistant Minister for Defence that Defence and DHA had mutually agreed to the proposed redevelopment of Seaward Village. This option was agreed by the then Assistant Minister for Defence.

From this point on, all communication between Defence, DHA and the key stakeholders was aimed at implementing the agreed redevelopment concept plan, namely 165 DHA houses and 141 lots for sale to the public.

#### **DHA's Communications Plan**

DHA's proposed concept plan was matured following consultation with:

- WA Department of Lands
- WA Department of Planning)
- City of Nedlands
- Friends of Allen Park
- Sayer Street residents
- Community Feedback (includes all interested parties, including Defence residents)
- ADF community
- Department of Defence, including key inputs from the Defence Security Review
- Special Operations Command
- Army HQ
- Defence Families of Australia

### Formal Interactions with ADF Members and Their Families

The following table outlines DHA consultation activities with ADF families, both within and external to Seaward Village:

| Stakeholder   | Date/s                          | Details   |
|---|---------------------------------|---|
| Focus Group study   | Late April 2015                 | Conducted by Horizon<br>Research.                                       |
| Survey issued by Special<br>Operations Command Head<br>Quarters (SOCOM) | May 2015                        | Conducted by Defence.   |
| Community information session<br>No. 1                                  | 10 June 2015                    | Associates Rugby Club -<br>approx. 170 attendees.                       |
| ADF member survey<br>(details below)                                    | Completed August/September 2015 | 400+ surveys issued.<br>61 responses from Seaward<br>Village residents. |
| ADF family information session  | 14 September 2015               | Gratwick Club - approx. 40 attendees.                                   |
| Community information session<br>No. 2                                  | 20 September 2015               | Presentation at Associates<br>Rugby Club.                               |

### Perth Region Survey of ADF Members

DHA conducted a detailed survey of Defence members posted to the entire Perth region in July/August 2015. A number of questions were provided only to residents of Seaward Village.

Specifically, Seaward Village residents were asked to what degree they were for or against the redevelopment. Of the 61 responses (from residents of Seaward Village):

- 59% supported a redevelopment
- 21% expressed no opinion
- 20% were against a redevelopment

#### **Local Interest Groups**

Local interest groups include:

- Friends of Allen Park. Friends of Allen Park are a community group that are part of the Urban Bushland Council of WA and are active in the local area. Their aim is to preserve a special pocket of coastal bushland in Swanbourne with a view to regenerate degraded areas, control erosion, remove exotic species and protect wildlife by improving the habitat for fauna, flora and fungi. DHA understands that they perceive the proposed development would negatively impact that goal.
- Swanbourne Coastal Alliance. Swanbourne Coastal Alliance is a community group that is part of the Urban Bushland Council of WA. Its mission is twofold:
  - To retain public access to coastal areas for the greater community.
  - To conserve flora, fauna, fungi, ecological communities and ecosystem processes, as well as the marine environment and coastal processes.

Its objective is to work with communities, local, state and federal government authorities to achieve positive planning and management outcomes for coastal environments.

DHA has requested a number of meetings with the Convenor of the Swanbourne Coastal Alliance. However a meeting has yet to take place.

• Sayer Street Residents. Sayer Street is one of the two access roads currently servicing Seaward Village. There are eight properties (non-Defence) on Sayer Street.

| Stakeholder                     | Date/s   | Details   |
|---------------------------------|--|---|
| Friends of Allen Park           | 27 Feb 2014<br>3 Feb 2015<br>8 Apr 2015<br>6 May 2015<br>20 May 2015 | Accompanied site walk through and meeting<br>Meeting<br>Advised DHA would seek Improvement Plan<br>Opportunities Workshop<br>Presentation of Draft Principles Plan  |
| Sayer St Residents              | 25 Aug 2015  | Attended by Sayer St residents, Mayor,<br>Deputy Mayor and Cr Nikola Horley   |
| Community Info Session<br>No. 1 | 10 Jun 2015  | Attended by DHA staff, and expert<br>consultants related to the specific areas of<br>Urban Design, Town Planning, Traffic<br>Engineering, Civil Engineering, Landscape<br>Architecture, and Architecture.<br>This session was also attended by a<br>representative from Defence.<br>Approx. 170 Attendees |
| Community Info Session<br>No. 2 | 20 Sep 2015  | Attended by DHA staff, and expert<br>consultants related to the specific areas of<br>Urban Design, Town Planning, Traffic<br>Engineering, Civil Engineering, Landscape<br>Architecture, and Architecture.   |

Interactions with local interest groups are detailed in the following table:

|  | Approx. 80 Attendees |
|--|----------------------|
|  |                      |

### **City of Nedlands**

| Date/s      | Details  |
|-------------|--|
| During 2014 | DHA held a number meetings with Mayor and senior Staff from City of Nedlands<br>Council, as well as senior representatives from Department of Planning and Department<br>of Lands in the WA Government.  |
| 5 Sep 2014  | A meeting was held between DHA, Department of Planning, Department of Lands, and<br>City of Nedlands to specifically discuss a redevelopment proposal. This meeting was<br>attended by executive members of the City of Nedlands                           |
| 7 Apr 2015  | DHA briefed City of Nedlands Council on its intention to seek a State Government level<br>Improvement Plan / Improvement Scheme process for the site.  |
| 9 Apr 2015  | DHA offered to City of Nedlands Councillors an opportunity and constraints workshop<br>on 5 May 2015, and then a subsequent presentation of a draft concept plan on 19 May<br>2015.<br>This offer was not taken up by City of Nedlands.                    |
| 26 May 2015 | DHA wrote a letter to Councillors further explaining rationale behind the improvement plan and provided another offer of a briefing  |
| 9 Jul 2015  | DHA wrote a letter to Councillors clarifying DHA's previous offers for briefing and provide a further offer of a briefing.   |
| 28 Jul 2015 | DHA's consultant wrote to Councillors (on DHA's behalf) regarding DHA's concerns around the proposed motion to close Sayer Street.   |
| 28 Jul 2015 | Council resolved to initiate process for disconnection of Sayer Street.  |
| 24 Aug 2015 | DHA met with Mayor, CEO & Director of Planning. DHA was invited to present the latest draft of the concept plan to City of Nedlands Council at its meeting on 15 September 2015.   |
| 25 Aug 2015 | On 22 May 2015 DHA received a letter from Sayer Street residents requesting a meeting.<br>A suitable time was agreed and a meeting occurred on 25 August 2015. The meeting with DHA was also attended by City of Nedlands Mayor, Deputy Mayor & Cr Horley. |
| 15 Sep 2015 | DHA presented a Concept Plan to City of Nedlands Councillors in advance of<br>Community Info Session No. 2   |
| 22 Sep 2015 | Statement & Letter to Councillors regarding Sayer St Road Closure and offer by DHA to meet.  |

This table details DHA's interactions with the City of Nedlands:

### **City of Nedlands Community Working Group**

In July 2015, City of Nedlands advertised for Community Members to join a working group regarding Seaward Village.

Whilst DHA was not initially invited to join this group, DHA is now a member, which also comprises three community members to represent the residents of Sayer Street, Friends of Allen Park, and residents of Seaward Village. Meetings have been held on the following dates:

- 6 October 2015
- 4 November 2015
- 2 December 2015

### **Overall Project Steering Group**

Following a meeting of key personnel from City of Nedlands, Department of Lands and Department of Planning on 5 September 2014, and subsequent meetings in December 2014, a Project Steering Group was set up consisting of representatives from:

- City of Nedlands
- WA Dept. of Lands
- WA Dept. of Planning

The Project Steering Group held a total of 10 meetings during 2015.

## Attachment 2

# **Redevelopment Concept**

The redevelopment of Seaward Village has been designed to provide a housing solution for the long term benefit of Defence members and their families posted to the Perth region.

The redevelopment involves the phased demolition of 153 existing homes, delivering 165 high quality architecturally designed, larger, and modern homes for ADF members and their families, along with new streets, parkland areas and a new childcare facility. The housing provided as part of the redevelopment is intended to be of the highest standard in DHA's housing portfolio, reflecting the unique nature of Seaward Village.

The 165 new houses would comprise 145 detached houses and 20 townhouses that would be built to last in the severe coastal environment. The houses will be a mix of double and single storey, three and four bedroom homes which will take advantage of modern sustainability features.

This redevelopment project would greatly improve the housing standard for the ADF members and their families residing in the village by bringing the quality into line with the contemporary standards and specific criteria that DHA provides to ADF members and their families posted to other localities in Australia.

DHA also intends to undertake significant works to improve the parks and recreation areas within the site, benefiting the ADF members and their families.

The existing child care centre would be replaced with a new, purpose built child care centre as a matter of priority. Subject to the necessary approvals, construction work was scheduled to commence on the new centre in 2016, with a seamless transfer of operation to occur in 2017 for all families using this service. Upon completion of the new centre, the old centre will close on a Friday, and the new centre would open on the following Monday, minimising disruptions.

As part of the redevelopment concept, approximately 141 new lots would be created (for sale to the public) in addition to the 165 houses to accommodate ADF members and their families. Construction on the private lots would be the responsibility of the purchasers. The purchasers, whether they be private buyers or builders, would be bound by design guidelines to ensure all future development of this land would be in keeping with the local area while maintaining the private development area.

As part of the agreement with Defence, DHA has planned that any ADF members and their families who reside in Seaward Village have the opportunity to remain in the village throughout the construction period. ADF members currently residing in Seaward Village who choose to live away from Seaward Village during the development period and wish to return at the completion of the redevelopment would be able to do so.

The development of Seaward Village is still subject to the relevant Western Australian statutory planning approvals. DHA is working in consultation with the Department of Defence, the Western Australian State Government, and the City of Nedlands.

The community would have opportunities to comment and provide input formally throughout these processes.

The proposed redevelopment of Seaward Village would be a multi-year, phased project, with timeframes planned (prior to the government review) as follows:

| Date/s           | Activity   |
|------------------|--|
| Mid 2016         | Construction of new child care centre scheduled<br>to begin (including demolition of a small<br>number of homes) |
| Early – mid 2017 | Existing child care centre scheduled to close<br>New child care centre complete and operational                  |
| Early – mid 2017 | Phased demolition and construction of new homes begins   |
| Late 2019        | First new Defence homes complete<br>Phased construction of new homes continues                                   |
| 2019 - 2023      | Sale of 141 lots to the public   |
| 2022             | Redevelopment of all 165 DHA homes completed   |

DHA has ceased works progressing the development option and therefore it is unlikely these dates would be achieved. The program will need to be updated should approval to proceed be granted.


#### **Cost and Time Savings**

The development's project budget is based on making Seaward Village the flagship housing standard for DHA and Defence.


If more modest housing specifications (project home), and open space works were to be undertaken, as well as reverting to a single stage development, the project could achieve significant cost savings.

These savings are outlined in the financial submission provided separately as commercial in confidence.

### **Current Concept Plan**

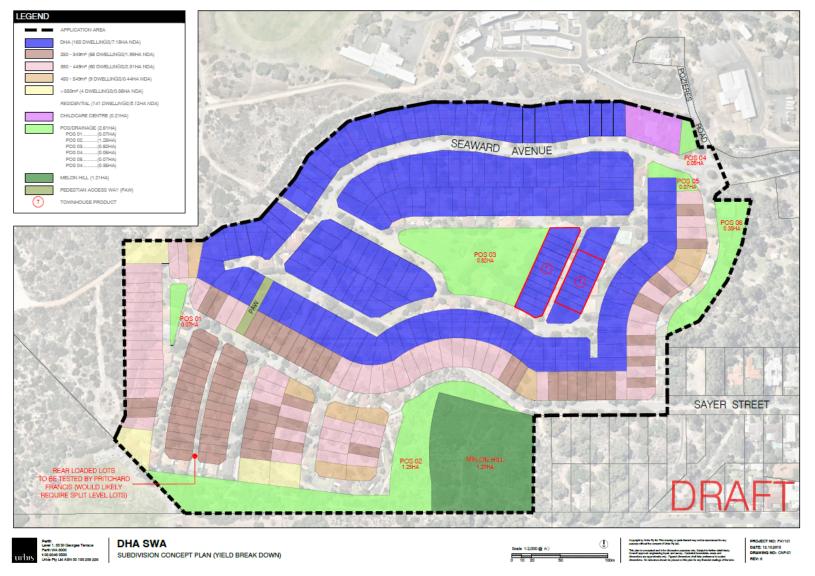

### Concept Plan – As Agreed in November 2014

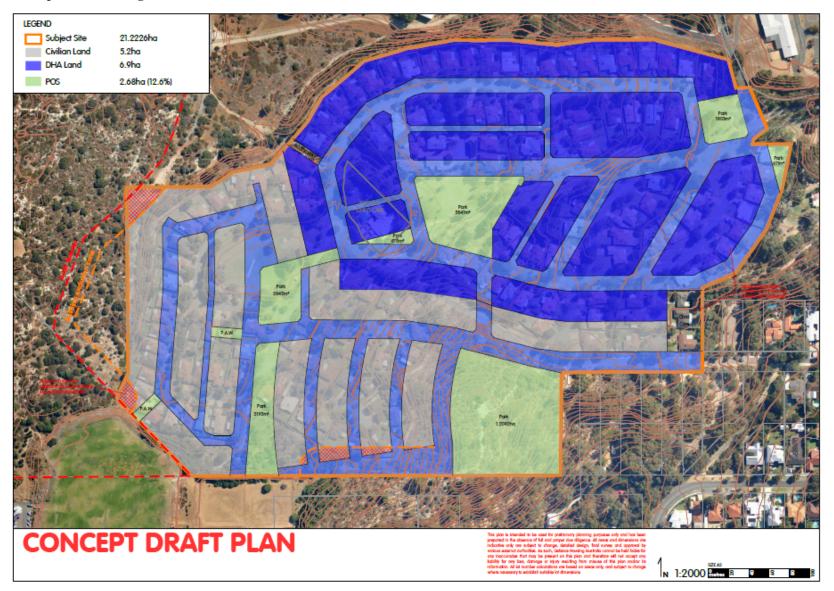

#### FOUO

| LIST OF SUBMISSIONS TO |
|------------------------|
| SEAWARD VILLAGE REVIEW |

| Submission<br>No | Date      | Name | Interest  | Opposed/<br>Supportive |
|------------------|-----------|------|---|------------------------|
| 1                | 13 Dec 15 | s47F | Swanbourne resident. Concerned about local amenity if development goes ahead                          | Opposed                |
| 2                | 15 Dec 15 | -    | s47F Concern about taxpayer money, security, social impact, native species, wild life                 | Opposed                |
| 3                | 17 Dec 15 | -    | Sayer St <sup>s47F</sup> concerned about impact on street,<br>environmental impact on Allen Park (AP) | Opposed                |
| 4                | 18 Dec 15 | +    | s47F     Concerned about impact on indigenous flora and fauna in Allen Park                           | Opposed                |
| 5                | 9 Dec 15  | -    | s47F Believes covenant must remain for Defence housing  | Opposed                |
| 6                | 19 Dec 15 | +    | s47F Concerned about impact on ADF families,<br>disruption during redevelopment and impact on AP      | Opposed                |
| 7                | 19 Dec 15 |      | s47F     Questions purpose of redevelopment and destruction of the area                               | Opposed                |
| 8                | 19 Dec 15 |      | s47F         Believe redevelopment is a bad proposal for Defence<br>and the neighbouring committee    | Opposed                |
| 8A               | 9 Jan 16  |      | Importance of natural settings and open green spaces for PTSD sufferers                               | Opposed                |

Disclosure Warning – This binder contains personal information that was collected from people making submissions as part of the Review. Information includes, for example, peoples' names and affiliations. The information should be managed in accordance with the Australian Privacy Principles under the Privacy Act 1988. No express consent to the public disclosure of their personal information has been obtained from the affected people.

| 9   | 17 Dec 15 | s47F | Requested meeting with LTGEN Evans to propose a new concept.<br>Discussion revealed this was outside of the Review Terms of Reference  | Met LTGEN<br>Evans on 13 |
|-----|-----------|------|--|--------------------------|
|     |           |      |  | Jan 16                   |
| 10  | 22 Dec 15 |      | s47F supports SAS families<br>preference for refurbishment, agrees security concerns, notes community<br>concerns about environment, agrees some scope for apartments for<br>couples, singles, notes Nedlands Council concerns re Sayer St | Opposed                  |
| 11  | 23 Dec 15 | -    | sources reclames council concerns to bayer st         s47F         Concerned about security, protection of         Allen Park and environment, the Covenant on the land. Support         refurbishment over redevelopment                  | Opposed                  |
| 11A | 15 Jan 16 |      | Following two meetings with LTGEN Evans complained about the appointment of someone from within Defence to conduct the Review, concerned that is only getting input from DHA   | Opposed                  |
| 12  | 27 Dec 15 | -    | Security concerns in relation to retaliation against SASR families   | Opposed                  |
| 13  | 29 Dec 15 |      | Local resident concerned about the environment and wishes to support<br>SASR people. Endorsed open letter to Senator Payne and Nedlands<br>Council's efforts to protect and preserve the Allen Park precinct                               | Opposed                  |
| 14  | 29 Dec 15 | -    | Local resident, <sup>s47F</sup> walk up Melon Hill. Endorsed open<br>letter to Senator Payne and Nedlands Council's efforts to protect and<br>preserve the Allen Park precinct   | Opposed                  |
| 15  | 31 Dec 15 |      | s47F<br>Concerned about poor communication, prefers refurbishment over<br>redevelopment because of los of yard sizes, parkland and amenities,<br>undesirability of 2 storey townhouses, social impact on Village<br>community              | Opposed                  |

| 16  | 3 Jan 16  | s47F | s47F Concerned about<br>impact on Allen Park, Sayer St and the environment, security for SASR<br>families   | Opposed |
|-----|-----------|------|---|---------|
| 17  | 3 Jan 16  |      | s47F Concerned about poor communication by DHA, acknowledges the need for SASR families to have good housing and security, thinks a less destructive option can be achieved   | Opposed |
| 18  | 3 Jan 16  | -    | s47F<br>Principally concerned about environmental implications of<br>redevelopment. Social, security and Covenant aspects also addressed.<br>Made a similar submission to WA Planning in Jul 15   | Opposed |
| 18A | 15 Jan 16 |      | Provided copy of presentation given at meeting in Perth attended by LTGEN Evans   |         |
| 19  | 4 Jan 16  |      | s47F     Outlined issues in relation to urban       design aspects of DHA plan  | Opposed |
| 20  | 4 Jan 16  |      | Endorsed letter to Senator Payne, Motion of City of Nedlands re<br>objections to DHA plans and supports closure of Sayer St   | Opposed |
| 21  | 4 Jan 16  |      | Concerns about impact on coastal environment<br>Critical of timing of Review and said it should be extended over Jan/Feb.<br>Concerned that insufficient time will be given to submissions and that<br>DHA will have a disproportionate input and influence. Questioned<br>impartiality of the Review Team. | Opposed |
| 21A | 16 Jan 16 | s47F | s47F is totally opposed to the introduction of private housing in SV, the   | Opposed |

|     |           |                         | DHA proposal will impose a completely unacceptable impact on the<br>bushland and amenity of the Allen Park precinct  |         |
|-----|-----------|-------------------------|--|---------|
| 22  | 4 Jan 16  | Confidential submission | Believe the proposal will adversely affect the quality of life of families in SV   | Opposed |
| 22A | 15 Jan 16 |                         | Supplementary submission after visit by LTGEN Evans to Perth.<br>Explanation about the DHA survey – respondents were not advised of<br>refurbishment option, they were only asked to comment on<br>redevelopment   |         |
| 23  | 4 Jan 16  | s47F                    | s47FConcerned about disruption and dislocationcaused to ADF personnel, decreased security, increase in traffic flow inSayer St, impact on Allen Park (AP), prefer the refurbishment option (lesscostly and less destructive)   | Opposed |
| 24  | 6 Jan 16  | -                       | s47FOpposed to proposal and<br>critical of measures adopted by DHA, ie lack of consultation and<br>misrepresentation of the site.Enclosed PDF photographic presentation of the site.   | Opposed |
| 25  | 6 Jan 16  |                         | s47F believes there are<br>major flaws in the current proposal and have identified a number of key<br>issues that need to be addressed before s47F could support the proposal  | Opposed |
| 26  | 7 Jan 16  |                         | Believes the safe, secure supportive environment of the Village<br>is comforting for families and deployed members. Impact on the primary<br>school will be extreme if the village is demolished and is a building site<br>for 5 yrs. About one third of the school children come from SV. | Opposed |

| 27 | 7 Jan 16 | s47F | s47F                         | Concerns about lack of respect by DHA                   | Opposed |
|----|----------|------|------------------------------|---|---------|
|    |          |      | towards ADF me               | mbers, poor planning and consultation by DHA,           |         |
|    |          |      | security, impact of          | on the broader community. Supports Nedland Council      |         |
|    |          |      | resolutions and o            | pen letter to Senator Payne. Supports submission to     |         |
|    |          |      | LTGEN Evans m                | ade by <sup>\$47F</sup> 18 Dec 15                       |         |
| 28 | 7 Jan 16 |      | s47F                         | Concerned about saving AP, disruption to ADF            | Opposed |
|    |          |      | families, sale of l          | and to civilians, building of roads, opposed to         |         |
|    |          |      | demolishment of              | SV houses   |         |
| 29 | 7 Jan 16 |      | Swanbourne resid             | dent. Questions demolition of houses built in 1991,     | Opposed |
|    |          |      | impact on securit            | y for families, concerned about social impact, supports |         |
|    |          |      | FOAP views on i              | mpact on Allen Park, believes ADF families have been    |         |
|    |          |      | ignored by DHA               | and don't have a voice. Believes Covenant should be     |         |
|    |          |      | established to pre           | event future use of the land                            |         |
| 30 | 7 Jan 16 |      | s47F                         | Concerned about   | Opposed |
|    |          |      | DHA processes a              | nd approach, believes the community was misled on the   |         |
|    |          |      |                              | ect from the outset and City of Nedlands was alienated. |         |
|    |          |      | Believes changes             | in the top echelons of DHA provide an opportunity to    |         |
|    |          |      | revisit the propos           |   |         |
| 31 | 7 Jan 16 |      | Swanbourne resid             | dent, concerned about DHA tactics at Sep 15 meeting.    | Opposed |
|    |          |      | Welcomes review              | V   |         |
| 32 | 8 Jan 16 |      | Swanbourne resid             | dent, concerned about effect on SASR personnel if DHA   | Opposed |
|    |          |      | proposal proceed             | s   |         |
| 33 | 8 Jan 16 |      | Advised <sup>s47F</sup> endo | orsed open letter to Senator Payne                      | Opposed |
| 34 | 8 Jan 16 |      | Swanbourne resid             | dent. Supports FOAP and FOAP Bush Group, concerned      | Opposed |
|    |          |      | about security, er           | vironment, resource wastage (bulldozing SV), traffic    |         |
|    |          |      | impact                       | ´`  |         |
| 35 | 8 Jan 16 |      | Swanbourne resid             | dent. Concerned about lack of consultation by DHA,      | Opposed |
|    |          |      | security for ADF             | families  | 1       |

| 36 | 9 Jan 16  | s47F | s47F          | concerned about preservation of Allen Park, traffic            | Opposed |
|----|-----------|------|---------------|--|---------|
|    |           |      | problems, la  | ack of consultation by DHA, believes redevelopment not         |         |
|    |           |      | necessary     |  |         |
| 37 | 9 Jan 16  |      | s47F          |  | Opposed |
|    |           |      |               | Opposed to changes that affect the Reserve. New                |         |
|    |           |      | housing unv   | welcome and unnecessary, increased traffic of concern          |         |
| 38 | 9 Jan 16  |      | s47F          | planting of trees in area                                      | Opposed |
|    |           |      | which is a s  | anctuary for birds and wildlife. There should be proper        |         |
|    |           |      | consultation  | n wrt development plans  |         |
| 39 | 9 Jan 16  |      | s47F          | lives near Swanbourne.   | Opposed |
|    |           |      | Concerned a   | about terms of reference, DHA proposal, operational needs,     |         |
|    |           |      | Governmen     | t (Federal and State) positions, Covenant on land, DHA         |         |
|    |           |      | costings, so  | cial impact, wants retention of SV solely for military housing |         |
| 40 | 9 Jan 16  |      | Swanbourne    | e resident, concerned about destruction of community           | Opposed |
|    |           |      | atmosphere    | of Swanbourne, reduction of the amenity for 'ordinary' folk,   |         |
|    |           |      | ADF person    | nnel being constrained from comment, prefers refurbishment     |         |
|    |           |      | option on cu  | urrent footprint   |         |
| 41 | 10 Jan 16 |      | Swanbourne    | e resident <sup>s47F</sup>                                     | Opposed |
|    |           |      |               | opposed to DHA proposal, concerned about                       |         |
|    |           |      | security, pla | an to demolish after only 25 yrs is flawed, increased traffic  |         |
|    |           |      | concerns      |  |         |
| 42 | 11 Jan 16 |      | s47F          | Concerned about  | Opposed |
|    |           |      | impact on se  | ecurity (both to Barracks and families in SV), noise buffer    |         |
|    |           |      |               | sal for civilian houses abutting MQs and the Barracks          |         |
|    |           |      | increases the | e likelihood of access to them. Seeks serious consideration of |         |
|    |           |      | the potentia  | l for increased security threat to families and barracks and   |         |
|    |           |      |               | tations to essential training arising from noise complaints by |         |
|    |           |      |               | no purchase proposed new housing in SV                         |         |
|    |           |      |               | · · · · ·  |         |

| 43 | 11 Jan 16 | s47F | Swanbourne resident. Concerned about lack of consultation by DHA,           | Opposed |
|----|-----------|------|---|---------|
|    |           |      | disempowerment of SASR families, security, seeks a more open process        |         |
|    |           |      | and consideration of work of SASR and increased terrorist risk              |         |
| 44 | 11 Jan 16 |      | Supports         s47F         AP concerns and concern for SASR families     | Opposed |
| 45 | 11 Jan 16 |      | s47F Concerned increased population will ruin                               | Opposed |
| _  |           |      | the unique characteristic of the precinct, lack of consultation by DHA,     | 11      |
|    |           |      | believes there are other ways to refurbish with destruction.                |         |
| 46 | 11 Jan 16 |      | Supported letter to Senator Payne, believes DHA process is flawed, bad      | Opposed |
| -  |           |      | planning and impacts on security of SAS and wider community                 | 11      |
| 47 | 11 Jan 16 |      | Swanbourne resident. Wants consideration given to security/safety of        | Opposed |
|    |           |      | SAS families, sale of land 'beggars belief.'                                | 11      |
| 48 | 11 Jan 16 |      | s47F  | Opposed |
|    |           |      | Concerned about   | 11      |
|    |           |      | impact on Baines Park   |         |
| 49 | 11 Jan 16 |      | Swanbourne resident, <sup>\$47F</sup> Concerned                             | Opposed |
|    |           |      | about SAS community, lack of empathy by DHA, preservation of                | 11      |
|    |           |      | bushland, prefers refurbishment option                                      |         |
| 50 | 12 Jan 16 |      | s47F Allen Park and Melon Hill. Does  | Opposed |
|    |           |      | not want the community to lose these. Concerned about increased traffic     |         |
|    |           |      | and consequent danger to children   |         |
| 51 | 12 Jan 16 |      | Supported letter to Senator Payne. Supports City of Nedlands efforts to     | Opposed |
|    |           |      | preserve the AP precinct, close part of Sayer St and objections to DHA      |         |
|    |           |      | proposal  |         |
| 52 | 12 Jan 16 |      | Swanbourne resident, concerned about security issues, loss of bushland,     | Opposed |
|    |           |      | long-term disruption of ADF families. Submission relates to traffic issues. |         |
|    |           |      | s47F  |         |
|    |           |      |   |         |
|    |           |      |   |         |

|    |           |      | s47F   |   |         |
|----|-----------|------|--|---|---------|
| 53 | 12 Jan 16 | s47F | Childcare centre does not nee<br>closing Saver St                                  | Wants to preserve the area and<br>is not in the interests of SAS personnel.<br>ed to be replaced. Supports local council in   | Opposed |
| 54 | 12 Jan 16 |      | Swanbourne resident, s47F<br>about preservation of AP, Me                          | Concerned<br>elon Hill, protection of SV for SAS housing  | Opposed |
| 55 | 12 Jan 16 |      |  | work being put into conservation of<br>P. Endorses the submission by <sup>\$47F</sup>   | Opposed |
| 56 | 12 Jan 16 |      | loss of security for ADF fami<br>breaching of covenant. All th<br>amenities intact | Melon Hill bushland, Allen Park<br>n black cockatoos in area. Concerned about<br>ilies, increase in traffic, loss of bushland,<br>at is necessary is refurbishment, leave local | Opposed |
| 57 | 13 Jan 16 |      | Swanbourne resident s47F   | traffic concerns, preservation of environment   | Opposed |
| 58 | 13 Jan 16 |      | Swanbourne resident, <sup>S47F</sup><br>likelihood of noise complaint<br>families  | concerned about expense,<br>is from new residents, uprooting of SAS   | Opposed |
| 59 | 13 Jan 16 |      | for demolition, refurbishment  | rned about security of SV, no business case<br>t more cost effective, disregard for ADF<br>nts during rebuild, environmental impact on  | Opposed |
| 60 | 13 Jan 16 |      |  | rned about cost of demolition/rebuild, social<br>y of life for Swanbourne residents, agree<br>s47F  | Opposed |

|    |           |      | s47F   |               |
|----|-----------|------|--|---------------|
| 61 | 13 Jan 16 | s47F | s47F resident, supported letter to Senator Payne, interested in retainin<br>the amenity of the area for sporting clubs, believes process is flawed, a<br>bad planning outcome that impacts on the SAS and wider community,<br>short sighted to mix private residences with ADF housing | g Opposed     |
| 62 | 13 Jan 16 |      | Swanbourne resident, FOAP have developed the parkland and it should<br>be retained, counter productive to demolish SV houses, refurbishment a<br>better option. Could be irreversible damage to local residents if the   | Opposed       |
| 63 | 14 Jan 16 |      | demolish and build option proceeds<br>Swanbourne resident, <sup>s47F</sup><br>Believes refurbishment is a cheaper option, also<br>concerned about security and social impact, covenant should remain   | Opposed       |
| 64 | 14 Jan 16 |      | Swanbourne resident. Believes there is a need for cost benefit analysis, need a minimally disruptive refurbishment program that satisfies community concerns   | Opposed       |
| 65 | 14 Jan 16 |      | Swanbourne residents <sup>s47F</sup> Seems unnecessarily detrimental to<br>ADF families and community to redevelop. Any need for higher density<br>accommodation could be met by selective redevelopment of some house   |               |
| 66 | 14 Jan 16 |      | Swanbourne residents. Prefer refurbishment option, expansion could lea<br>to extra traffic, hoons and socially irresponsible people and possibly Sta<br>Housing. SV homes are too good to destroy. Does not want reduction in<br>park, flora/fauna, Carnaby cockatoo problem           | d Opposed     |
| 67 | 14 Jan 16 |      | Swanbourne resident. Concerned about environmental and security matters and safety for <sup>\$47F</sup> children with increased traffic in the area. Say Street should not be an access road   | Opposed<br>er |
| 68 | 14 Jan 16 |      | s47F concern<br>about retention issues if proposal goes ahead. SASR need happy home<br>lives in SV   | ed Opposed    |

| 69 | 14 Jan 16 | s47F         | s47F Concerned about impact on fragile   | Opposed |
|----|-----------|--------------|--|---------|
|    |           |              | coastline, fauna and flora, increased traffic, reshaping of the natural  |         |
|    |           |              | environment and clearing of native habitat. Believe DHA have ignored   |         |
|    |           | _            | community concern  |         |
| 70 | 14 Jan 16 |              | s47F Believes DHA proposal is not in the interests of  | Opposed |
|    |           | Ļ            | our soldiers   |         |
| 71 | 15 Jan 16 |              | s47F Believes DHA profit is foremost   | Opposed |
|    |           |              | consideration in the proposal. Supports refurbishment, concerned about   |         |
|    |           |              | security and preservation of sound buffer to allow SASR training and   |         |
|    |           |              | operational requirements to continue   |         |
| 72 | 15 Jan 16 |              | Swanbourne resident. Objects to redevelopment on Integrity and Ethical   | Opposed |
|    |           |              | grounds. Houses should be refurbished not pulled down  |         |
| 73 | 15 Jan 16 |              | s47F complained about timing   | Opposed |
|    |           |              | of review, DHA process, supports SASR families, favours refurbishment  |         |
|    |           |              | over development, concerns about traffic in Sayer St, protection of bush   |         |
|    |           |              | land, public open spaces, proposed vesting of bushland into local Council,   |         |
|    |           | _            | security concerns of ADF families.   |         |
| 74 | 15 Jan 16 |              |  | Opposed |
|    |           |              | Concerned about conservation of the environment,   |         |
|    |           | _            | loss of green space and wildlife in area   |         |
| 75 | 15 Jan 16 |              | Swanbourne resident. Favours refurbishment on grounds of support for   | Opposed |
|    |           |              | SAS families, security, maintain the original purpose of the land, SAS   |         |
|    |           | L            | should get good housing given what they do for countrySwanbourne residentsSwanbourne residentsStartEndorse letter to Senator Payne and |         |
| 76 | 15 Jan 16 |              | Swanbourne residents <sup>\$47F</sup> Endorse letter to Senator Payne and  | Opposed |
|    |           |              | endorse Nedlands Council motions. Concerned for SASR families,   |         |
|    |           |              | security issues, impact on traffic, Allen Park, flora and fauna, etc   |         |
| 77 | 15 Jan 16 | Confidential | Swanbourne residents. Support SASR families, concerned about loss of   | Opposed |
|    |           | submission   | parkland, traffic issues on Sayer St, SV residents are temporary and local   |         |
|    |           |              | residents are permanent – they are concerned about the impact on the   |         |

|     |           |      | values of s47F homes   |         |
|-----|-----------|------|--|---------|
| 78  | 15 Jan 16 | s47F | s47F<br>Sayer St residents. Concerned <sup>s47F</sup> property will devalue and also oppose  | Opposed |
| 78A | 15 Feb 16 |      | development on a range of grounds. Would support any proposal that met<br>the needs of the ADF families, involves the City of Nedlands in the  |         |
|     |           |      | planning process, honours and implements existing motions of Nedlands<br>Council, preserves and enhances the green corridor, retains or strengthens<br>the protection provided by the Covenant   |         |
| 79  | 15 Jan 16 | -    | s47F<br>s47F Does not want land 'sold off,<br>wants protection for SAS families and prefers refurbishment option   | Opposed |
| 80  | 15 Jan 16 |      | Cottesloe resident. Pleased with meeting held by LTGEN Evans with<br>FOAP, felt their concerns were being heard. Major concern is welfare for<br>SASR families and pleased to hear their welfare/security is paramount<br>with the Review.                 | Opposed |
| 81  | 15 Jan 16 |      | s47F Wishes to preserve Allan Park and<br>Melon Hill, favours refurbishment option, disappointed by DHA<br>presentations   | Opposed |
| 82  | 18 Jan 16 | -    | s47F<br>Concerned about conservation of Allen Park and Melon Hill as a<br>community resource   | Opposed |
| 83  | 20 Jan 16 |      | s47F<br>about (1) maintenance of security if development goes ahead; (2) New   | Opposed |
|     |           |      | civilian residents may seek increasing restrictions on SASR training and<br>preparations for Operations; (3) Social impact – SV is a supportive<br>environment for families who experience long absences of a serving<br>member. The Covenant must remain. |         |

| 84                                     | 20 Jan 16      | s47F | s47F an objective and<br>transparent approach to achieving a mutually successful outcome   | Advised that<br>proposal<br>is predicated<br>on the<br>Minister's<br>decision on<br>the Review |
|--|----------------|------|--|--|
|  | 4-16 Jan<br>16 |      | <ul> <li>Submission supports:         <ul> <li>Letter to Senator Payne</li> <li>Nedlands Council motion to protect and preserve Allen Park precinct;</li> <li>And seeks further consideration of traffic issues on Sayer St and other existing local roads, bushland, public open space increases, pedestrian and cycle access, etc</li> <li>Endorsed by<sup>\$47F</sup> people. The main themes/areas of concern expressed were:                 <ul> <li>Welfare of the Defence families</li> <li>Environmental concerns</li> <li>Local amenity</li> </ul> </li> </ul> </li> </ul> | Opposed  |
| Background<br>Reading<br>from<br>ASASA | 14 Dec 15      |      | Provided historical information for background reading   | Opposed  |
|  | Jan 16         |      | Notes from Presenters at Friends of Allen Park meeting with LTGEN<br>Evans on 14 Jan 16  | Opposed  |
