Project Schedule - Phases 6 & 7
ADI Mulwala Contamination Management Project

Revision E 10-06-03
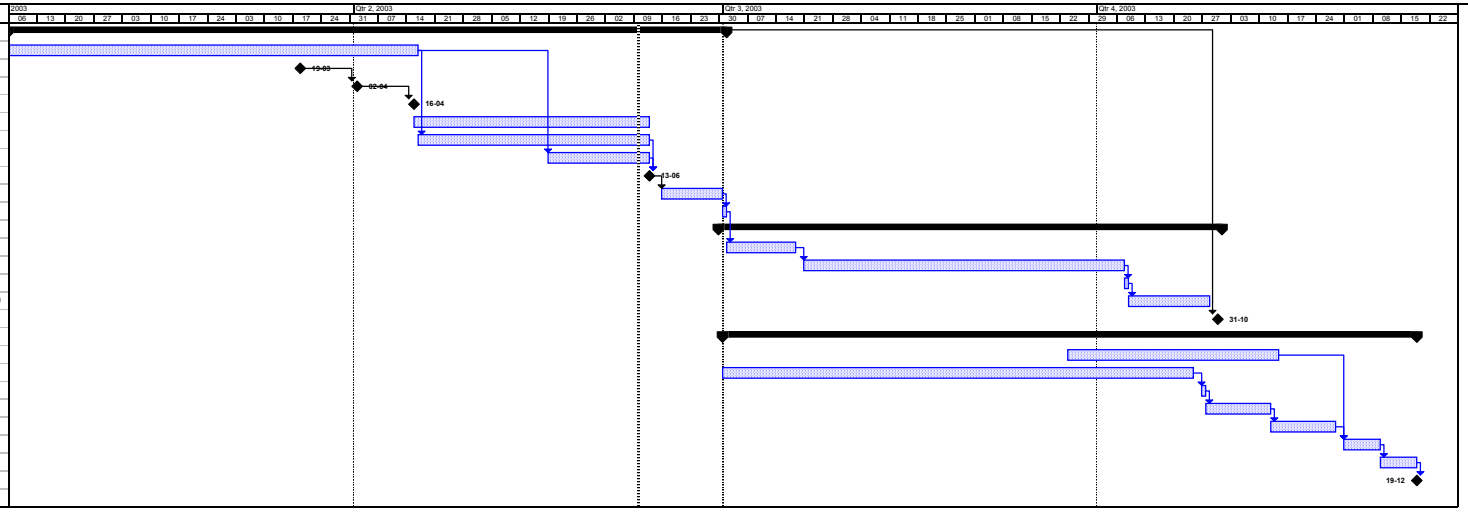
ID	Task Name
1	**Phase 6 – Remediation Feasibility**
2	Evaluate Remediation Technologies (concurrent with groundwater modelling)
3	Remediation team conference call 1
4	Remediation team conference call 2
5	Remediation team conference call 3
6	Stakeholder Consultation
7	Prepare Remediation Feasibility Study Report
8	Prepare Proposal for Bench Scale Trials
9	Issue Remediation Feasibility Report and Proposal for Bench Scale Trials
10	Auditor Review
11	Approve Bench Scale Trial
12	**Variation - Bench Scale Pilot Study (if required)**
13	Deliver Aquifer Material and Water and Begin Bench Scale Trials
14	Undertake Bench Scale Trial
15	Deliver Report for Bench Scale Trial
16	Undertake Additional Groundwater Modelling of the Prefered Strategy (if required)
17	Final Progress Payment for Phase 6
18	**Phase 7 – Contaminant Management Plan Preparation**
19	Design and Costing of Prefered Treatment Strategy
20	Preparation of CMP
21	Submit Draft CMP to Auditor
22	Stakeholder Consultation
23	Prepare Final CMP
24	Auditor / EPA Review
25	Prepare Final CMP
26	Final Progress Payment and Completion Date
27	**Commencement of CMP Implementation January 2004**
