

## PRICE AND PAYMENTS


- 1.1 Attachment B consists of the following Annexes:
- A. Price and Delivery Schedule
  - B. Schedule of Payments
  - C. Adjustments
  - D. Schedule of Further Quantities and Optional Extras (Not Used)
  - E. Schedule of Unit and NTE Prices
  - F. Incentive Payments (Not Used)
  - G. Rates for Survey and Quote Services

**INTENTIONALLY LEFT BLANK**

Serial 2

Table 1 Price Schedule


ITEM	ITEM DESCRIPTION	QTY	ITEMS SOURCED IN AUSTRALIA (in SAUD)	UNIT PRICE	UNIT PRICE DUTY FREE	UNIT PRICE DUTY PAID	CUSTOMS DUTY (in SAUD)	UNIT PRICE DUTY FREE	UNIT PRICE DUTY PAID	GST APPLICABLE (in SAUD)	UNIT PRICE GST INCLUSIVE	ITEMS SOURCED IN AUSTRALIA (in SAUD)	TOTAL	PRICE	TOTAL ITEM PRICE GST INCLUSIVE	DELIVERY POINT	RELATED DELIVERY ID Nos Ref. Table 2	VALUE OF LOCAL CONTENT (in SAUD)	TOTAL ITEM PRICE (in SAUD) excluding GST	VALUE OF LOCAL CONTENT (including GST)
(a)	WLR Contract	(b)	ITEMS SOURCED IN AUSTRALIA (in SAUD) (c)	UNIT PRICE DUTY FREE (d)	UNIT PRICE DUTY FREE (e)	UNIT PRICE DUTY PAID (f)	CUSTOMS DUTY (in SAUD) (g)	UNIT PRICE DUTY FREE (h)	UNIT PRICE DUTY PAID (i)	GST APPLICABLE (in SAUD) (j)	UNIT PRICE GST INCLUSIVE (k)	ITEMS SOURCED IN AUSTRALIA (in SAUD) (l)	TOTAL (m)	PRICE (n)	TOTAL ITEM PRICE GST INCLUSIVE (o)	DELIVERY POINT (p)	RELATED DELIVERY ID Nos Ref. Table 2 (q)	VALUE OF LOCAL CONTENT (in SAUD) (r)	TOTAL ITEM PRICE (in SAUD) excluding GST (s)	VALUE OF LOCAL CONTENT (including GST) (t)

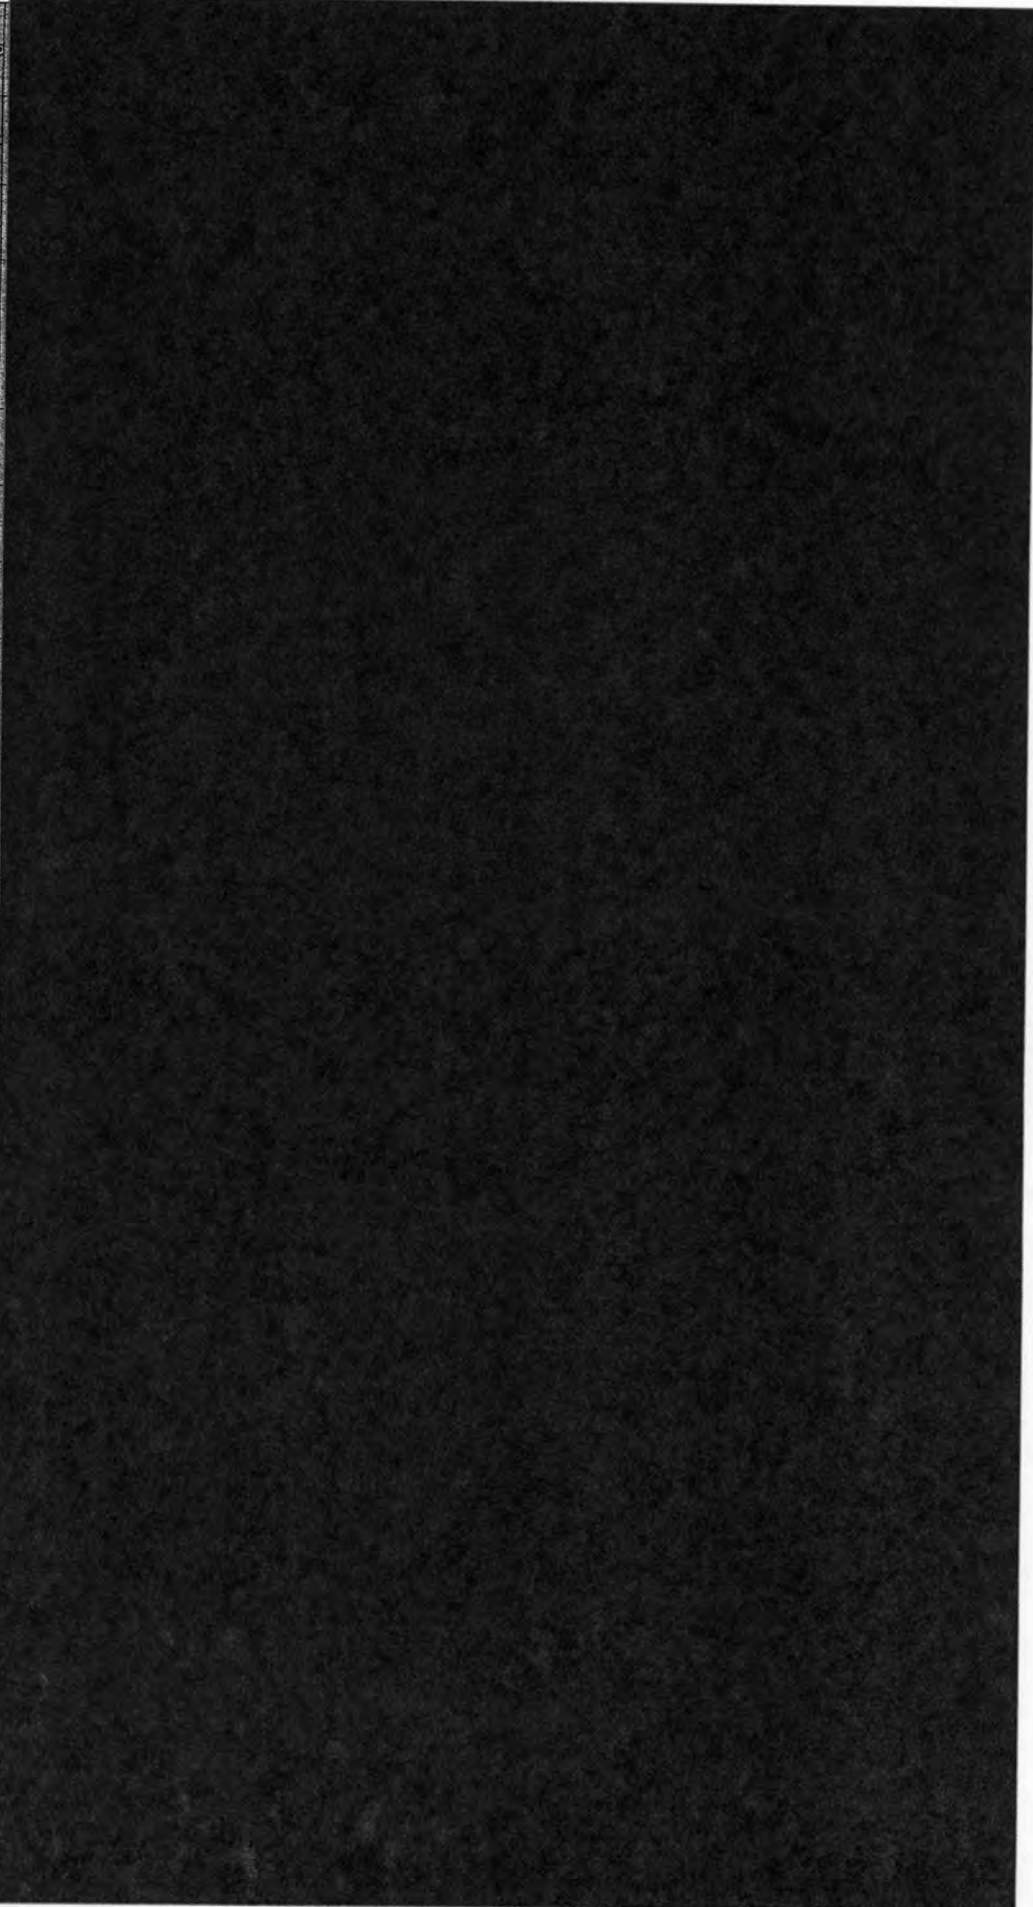

OR  
 PK  
 BAI

PRICE AND DELIVERY SCHEDULE

ITEM	ITEM DESCRIPTION	QTY	ITEMS SOURCED IN AUSTRALIA (in SAUDI GST Exclusive)	UNIT PRICE	ITEMS SOURCED	UNIT PRICE	UNIT PRICE	CUSTOMS DUTY (in SAUDI)	UNIT PRICE	GST APPLICABLE (in SAUDI)	UNIT PRICE	TOTAL	PRICE	DELIVERY POINT	RELATED DELIVERY ITEM	VALUE OF CONTRIBUTION (in SAUDI)	TOTAL ITEM PRICE (in SAUDI excluding GST)	VALUE OF LOCAL CONTRIBUTION (in SAUDI excluding GST)	
			ITEMS SOURCED IN AUSTRALIA (in SAUDI GST Exclusive)	UNIT PRICE DUTY FREE	ITEMS	UNIT PRICE DUTY FREE	UNIT PRICE DUTY FREE	CUSTOMS DUTY (in SAUDI)	UNIT PRICE DUTY PAID		UNIT PRICE GST INCLUSIVE	ITEMS SOURCED IN AUSTRALIA (in SAUDI)	Foreign Currency Component						
													Foreign Currency Component (SAUDI component)						

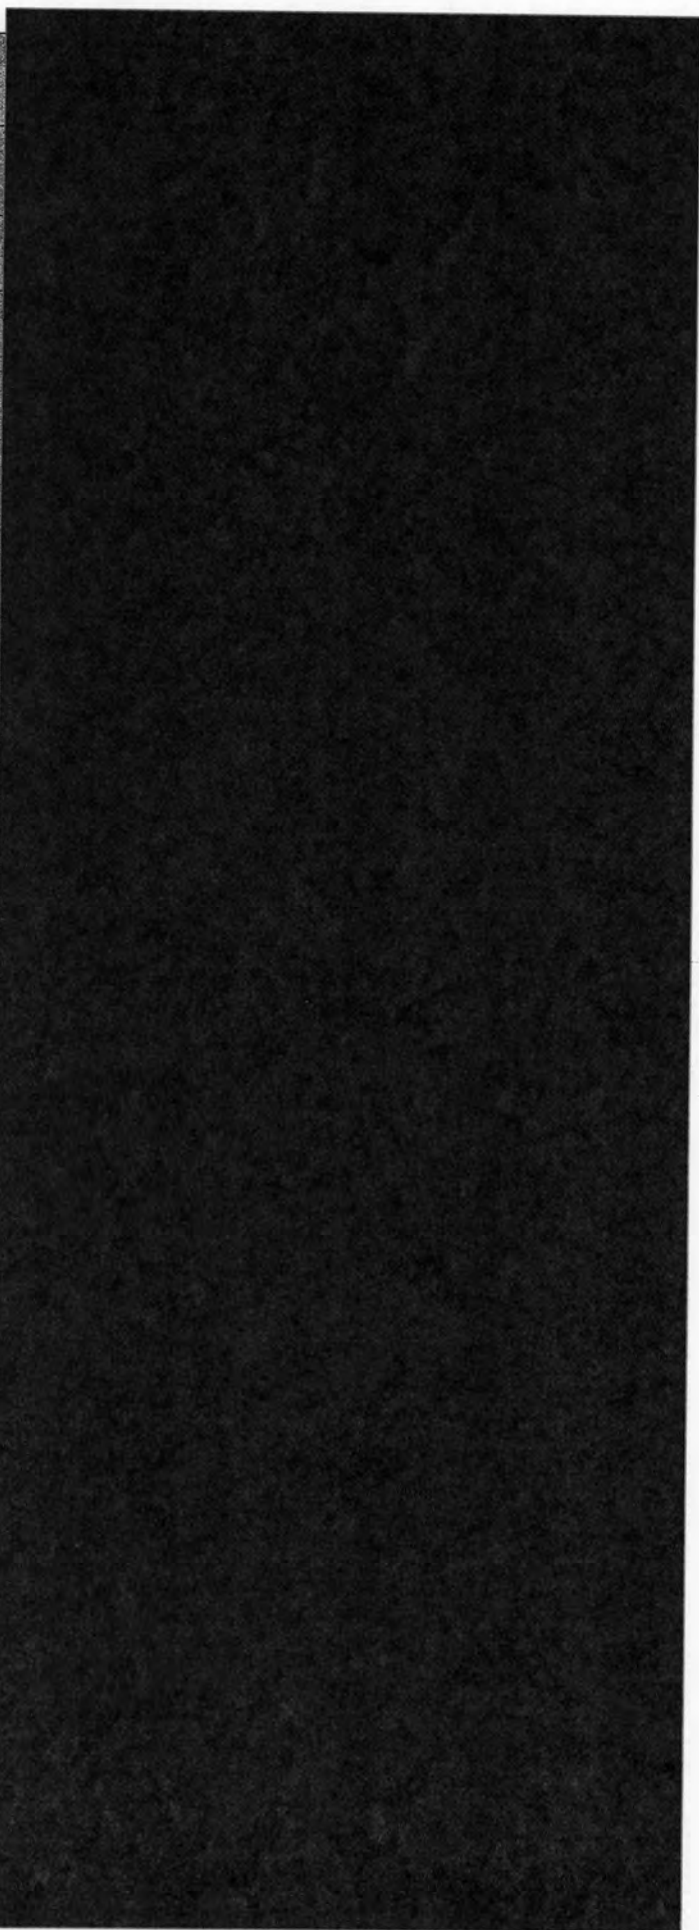

DR PK 842

PRICE AND DELIVERY SCHEDULE

Serial 4

Table 2 Delivery Schedule

Deliverable ID No	Deliverable Description	Delivery Point	Delivery Date Weeks from ED
(a)	(b)		(c)
1	Mobilisation Payment	LAND 58-3 Project Office	ED
2	CDRL - Contract Master Schedule	LAND 58-3 Project Office	ED + 4
3	CDRL - CWBS	LAND 58-3 Project Office	ED + 4
4	CDRL - Earned Value Management Plan	LAND 58-3 Project Office	ED + 4
5	CDRL - Project Management Plan	LAND 58-3 Project Office	ED + 4
6	CDRL - Project Start Up Plan	LAND 58-3 Project Office	ED + 4
7	CDRL - Systems Engineering Management Plan	LAND 58-3 Project Office	ED + 4
8	CDRL - Quality Plan	LAND 58-3 Project Office	ED + 4
9	CDRL - Risk Management Plan	LAND 58-3 Project Office	ED + 4
10	Simulator Software Specification	LAND 58-3 Project Office	ED + 8
11	System Specification	LAND 58-3 Project Office	ED + 13
12	SRR of Simulator	Raytheon Facility Melbourne	ED + 13
13	System Requirements Review	Raytheon Facility Melbourne	ED + 13
14	Procure Simulator Parts	LAND 58-3 Project Office	ED + 17
15	System Definition Review	Raytheon Facility Melbourne	ED + 17
16	Hardware, Software, Integration Test (HSIT)	Raytheon Facility Brisbane	ED + 21
17	Preliminary Design Review	Raytheon Facility Brisbane	ED + 26
18	Procure ROCS Hardware	LAND 58-3 Project Office	ED + 30
19	Conduct Simulator Training Verification	Raytheon Facility Brisbane	ED + 39
20	Procure ROCS Software	LAND 58-3 Project Office	ED + 43
21	Detailed Design Review	Raytheon Facility Brisbane	ED + 47
22	Procure S and T Mods Kits & Parts	LAND 58-3 Project Office	ED + 47
23	Initial Power Up and 1st Stage Tests	Raytheon Facility Brisbane	ED + 56
24	Installation of Simulator	S of Arty Puckapunyal	ED + 61
25	TRR of WLR 1	Raytheon Facility Brisbane	ED + 61
26	Verification of Maintenance Manuals	LAND 58-3 Project Office	ED + 65
27	Verification of Simulator	S of Arty Puckapunyal	ED + 65
28	Verification of WLR 1	S of Arty Puckapunyal	ED + 74
29	Acceptance of Simulator	S of Arty Puckapunyal	ED + 78
30	Acceptance of WLR 1	S of Arty Puckapunyal	ED + 78
31	Acceptance of WLR 2	Raytheon Facility Brisbane	ED + 80
32	Conduct Maintainer Conversion Course	S of Arty Puckapunyal	ED + 80
33	Conduct Operator Radar Course	S of Arty Puckapunyal	ED + 80
34	Acceptance of WLR 3	Raytheon Facility Brisbane	ED + 82
35	Acceptance of WLR 4	Raytheon Facility Brisbane	ED + 96
36	Acceptance of WLR 5	Raytheon Facility Brisbane	ED + 113
37	Acceptance of WLR 6	Raytheon Facility Brisbane	ED + 117
38	Acceptance of WLR 7	Raytheon Facility Brisbane	ED + 121

SCHEDULE OF PAYMENTS

Serial 5

Mobilisation Payment description	Mobilisation Payment Date	Amount of Mobilisation Payment				Total AUD Equivalent (GST Exclusive)	Total AUD Equivalent (GST Amount)
		SAUD (GST Exclusive)	USD	EUR	SAUD (GST Amount)		
Mobilisation Payment	Effective Date (ED)						

Milestone ID No	Milestone Description	Milestone Type	Milestone Date	Value of Milestone				Amount of Milestone Payment				Total AUD Equivalent (GST Exclusive)	Total AUD Equivalent (GST Amount)	Certification	
				SAUD (GST Exclusive)	USD	EUR	SAUD (GST Exclusive)	USD	EUR	SAUD (GST Exclusive)	USD				EUR
1	Mobilisation Payment		ED												Acceptance
2	CDRL - Contract Master Schedule		ED + 8												Acceptance
3	CDRL - CWBS		ED + 8												Acceptance
4	CDRL - Earned Value Management Plan		ED + 8												Acceptance
5	CDRL - Project Management Plan		ED + 8												Acceptance
6	CDRL - Project Start Up Plan		ED + 8												Acceptance
7	CDRL - Systems Engineering Management Plan		ED + 8												Acceptance
8	CDRL - Quality Plan		ED + 8												Acceptance
9	CDRL - Risk Management Plan		ED + 8												Acceptance
10	Simulator Software Specification		ED + 12												Acceptance
11	System Specification		ED + 17												Acceptance
12	SRR of Simulator		ED + 17												Acceptance
13	System Requirements Review		ED + 17												Acceptance
14	Procure Simulator Parts		ED + 17												Acceptance
15	System Definition Review		ED + 21												Acceptance
16	Hardware, Software, Integration Test (HSIT)		ED + 25												Acceptance
17	Preliminary Design Review		ED + 30												Acceptance
18	Procure ROCS Hardware		ED + 34												Acceptance
19	Conduct Simulator Training Verification		ED + 43												Acceptance
20	Procure ROCS Software		ED + 47												Acceptance
21	Detailed Design Review		ED + 51												Acceptance
22	Procure S and T Mods Kits & Parts		ED + 51												Acceptance
23	Initial Power Up and 1st Stage Tests		ED + 60												Acceptance
24	Installation of Simulator		ED + 65												Acceptance
25	TRR of WLR 1		ED + 65												Acceptance
26	Verification of Maintenance Manuals		ED + 69												Acceptance
27	Verification of Simulator		ED + 69												Acceptance
28	Verification of WLR 1		ED + 78												Acceptance
29	Acceptance of Simulator		ED + 82												Acceptance
30	Acceptance of WLR 1		ED + 82												Acceptance
31	Acceptance of WLR 2		ED + 84												Acceptance
32	Conduct Maintainer Conversion Course		ED + 84												Acceptance
33	Conduct Operator Radar Course		ED + 84												Acceptance
34	Acceptance of WLR 3		ED + 86												Acceptance
35	Acceptance of WLR 4		ED + 100												Acceptance
36	Acceptance of WLR 5		ED + 117												Acceptance
37	Acceptance of WLR 6		ED + 121												Acceptance
38	Acceptance of WLR 7		ED + 125												Acceptance
	<b>TOTAL</b>														Final Acceptance
	<b>(Including Mobilisation Payment)</b>														

DR  
B-81
